




GOVERNMENT OF PAKISTAN
MINISTRY OF COMMUNICATIONS
NATIONAL HIGHWAY AUTHORITY





**Procurement Status of Annual Maintenance Plans
2017-18, 2018-19 , 2019-20 & 2020-21**

As on 13th July 2021



Details of Works under AMP 2017-18, 2018-19, 2019-20 and 2020-21

Maintenance of NHA Network West Zone (Balochistan Province)

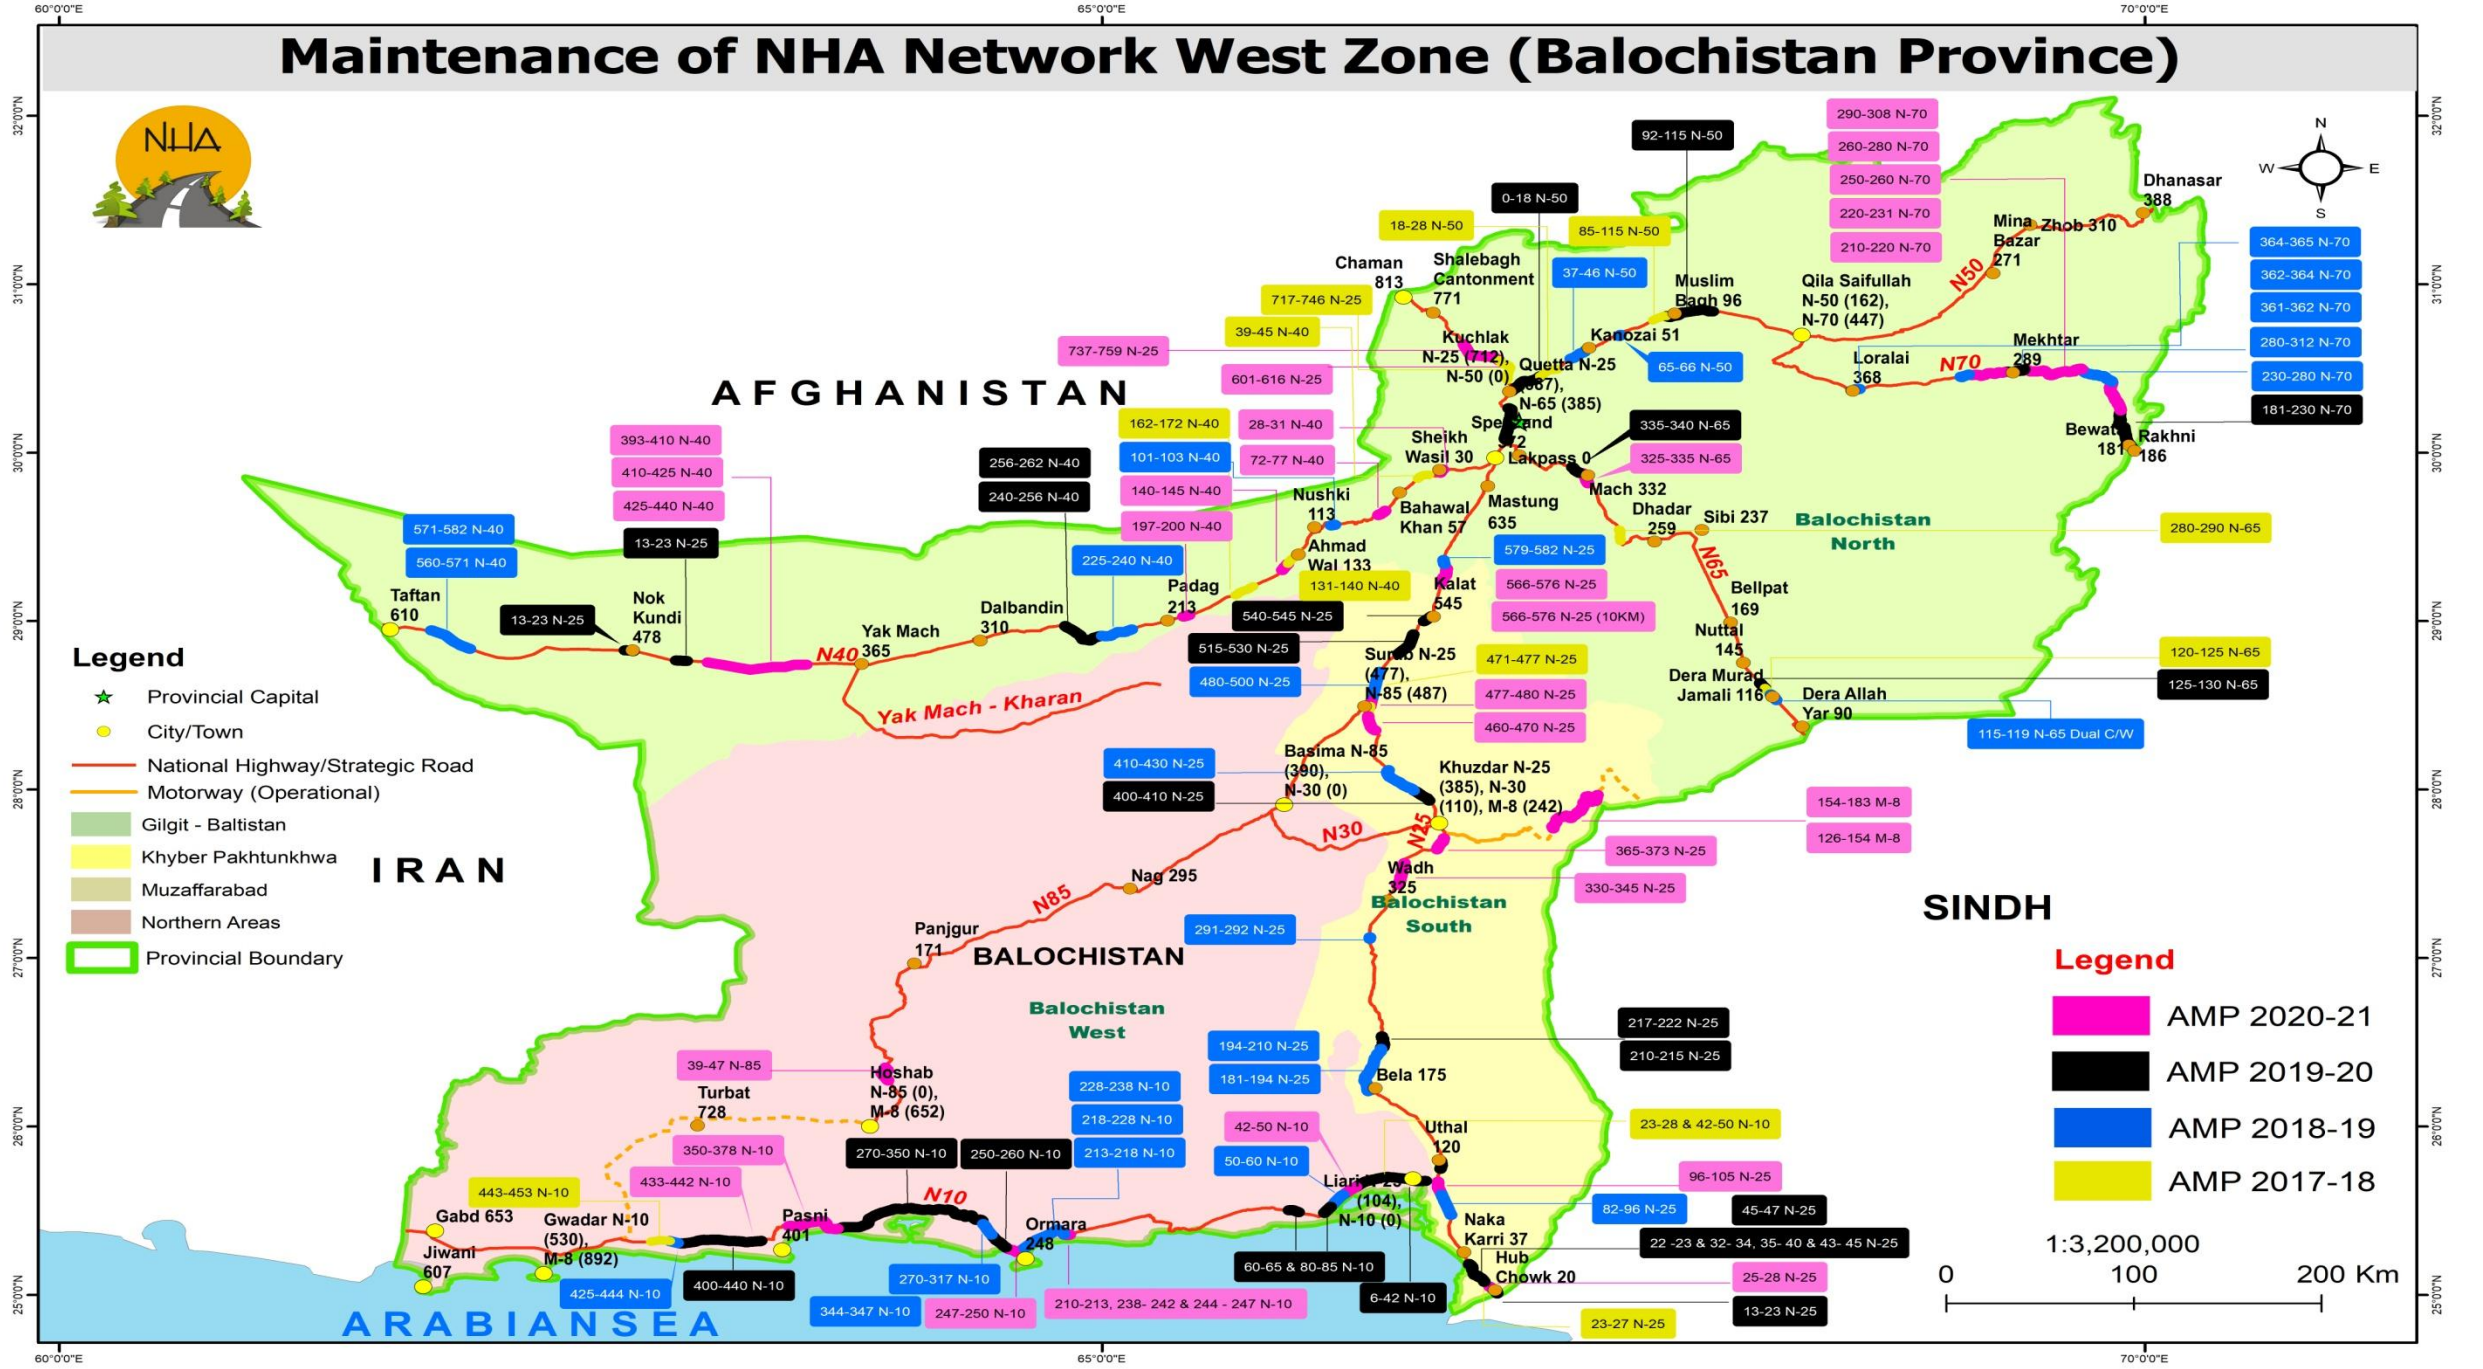

Legend

- ★ Provincial Capital
- City/Town
- National Highway/Strategic Road
- Motorway (Operational)
- Gilgit - Baltistan
- Khyber Pakhtunkhwa
- Muzaffarabad
- Northern Areas
- Provincial Boundary

Legend

- AMP 2020-21
- AMP 2019-20
- AMP 2018-19
- AMP 2017-18

1:3,200,000
0 100 200 Km

Balochistan – North (2017-18)

Sr No	Route	Location		Contractor	Completion Date	Cost	Progress
		From	To				
1	N-25	717.000	746.000	M/s Zarif Khan Hussainzai JV Ibrahim & Sons	20.03.2021	136,241,304	80%
2	N-40	39.000	45.000	M/s H.A Hameed Bangulzai JV M.Akber Shawani	30.08.20	83,225,270	100%
3	N-40	131.000	140.000	M/s Zarif Khan Hussainzai JV Ibrahim & Sons	04.06.2021	117,753,133	0%
4	N-40	162.000	172.000	M/s Zarif Khan Hussainzai JV Ibrahim & Sons	04.06.2021	130,764,915	0%
5	N-50	85.000	115.000	Shah Builders	15.01.2020	152,883,908	100%
6	N-50	18.000	28.500	M/s Shah Builders JV HRK	15.01.2020	148,402,214	100%
7	N-65	120.000	125.000	M/s H.A Hameed Bangulzai JV M.Akber Shawani	26.06.2020	41,416,053	100%
8	N-65	280.000	290.000	M/s H.A Hameed Bangulzai JV M.Akber Shawani	07.05.2020	83,454,137	100%

Balochistan North (2018-19)

Sr No	Route	Engr Est	Location		Contractor Name	Contract Cost	Completion Date	Progress
			From	To				
1	N-50	155.932	37+650	46+00	Cancelled	94.572	-	Contract Cancelled
2	N-70	91.918	230+00	280+00	M/s Haji Matiullah & Brthers	56.729	08.03.2022	35%
3	N-70	71.487	280+00	312+00	M/s Haji Matiullah & Brthers	42.641	08.03.2022	30%
4	N-50	40.087	65+00	66+00	M/s Sardar Noor Ahmed Kehtran	23.336	10.09.2021	100%
5	N-70	173.026	361+00	362+600	M/s Haji Abdul Rauf & Brothers JV Hamayoun & Brothers	102.085	07.06.2021	40%
6	N-70		362+600	364+100				
7	N-70		364+100	365+700				
8	N-40	250.983	225+00	240+00	Under Procurement			
9	N-40	181.804	560+00	571+00	M/s Haji Abdul Rauf & Brothers JV Hamayoun & Brothers	107.719	17.08.2021	35%
10	N-40	181.479	571+00	582+00	M/s Haji Abdul Rauf & Brothers JV Hamayoun & Brothers	107.434	17.08.2021	35%
11	N-25	111.204	579+00	582+00	M/s Saifullah Muhammad Shahi	72.28	Under Award process	
12	N-65 Dual C/W	232.324	115+00	119+500	M/s Karamullah Const. Co.	167.738	20.03.2021	100%

Balochistan North (2019-20)

Sr No	Scheme	Engineer's Estimate	T.S Date	Procurement Status		Award Date (Expected)	Completion Time	Completion Date (Expected)
				TBER Status	PBER Status			
1	N-25 - Km 13+00 - 23+00	237.642	3/12/2020	Works annulled due to launching of the Project on Quetta Western Bypass				
2	N-25 - Km 00+00 - 13+00	210.518	3/12/2020					
3	N-40 - Km 478+00 - 481+00	54.442	5/11/2020	Approved	Under Process	Aug-21	178 Days	Feb-2022
4	N-40 - Km 450+00 - 456+00	118.822	3/12/2020	Approved	Under Process	Aug-21	178 Days	Feb-2022
5	N-50 - Km 00+00 - 18+00	274.771	3/12/2020	Approved	Under Process	Aug-21	178 Days	Feb-2022
6	N-50 - Km 92+500 - 115+00	345.855	3/12/2020	Approved	Under Process	Aug-21	178 Days	Feb-2022
7	N-70 - Km 181+00 - 230+00	110.010	3/12/2020	Approved	Under Process	Aug-21	178 Days	Feb-2022
8	N-65 - Km 125+00 - 130+00	122.378	3/12/2020	Approved	Under Process	Aug-21	178 Days	Feb-2022
9	N-40 - Km 240+00 - 256+00	480.494	3/12/2020	Approved	On Under Process	Aug-21	178 Days	Feb-2022
10	N-40 - Km 256+00 - 262+500	187.932	3/12/2020	Approved	Under Process	Aug-21	178 Days	Feb-2022
11	N-65 - Km 335+00 - 340+00	149.786	3/12/2020	Approved	Under Process	Aug-21	178 Days	Feb-2022

Balochistan North (2020-21)

Sr No	Scheme	Eng Est (Million)	T.S Date (Expected)	Procurement Status	Award Date (Expected)	Completion Time	Completion Date (Expected)
1	Km 393+00-410+00 N-40	283.472	20/5/2021	To be Procured	20/10/2021	178 Days	30.06.2022
2	Km 410+000-425+000 on N-40	250.07	20/5/2021	To be Procured	20/10/2021	178 Days	30.06.2022
3	Km 425+000-440+000 on N-40	250.07	20/5/2021	To be Procured	20/10/2021	178 Days	30.06.2022
4	Km 325+000-335+000 on N-65	205.19	20/5/2021	To be Procured	20/10/2021	178 Days	30.06.2022
5	Km 28+000-31+000 on N-40	82.578	20/5/2021	To be Procured	20/10/2021	178 Days	30.06.2022
6	Km 72+000-77+000 on N-40	136.764	20/5/2021	To be Procured	20/10/2021	178 Days	30.06.2022
7	Km 140+000-145+000 on N-40	138.74	20/5/2021	To be Procured	20/10/2021	178 Days	30.06.2022
8	Km 566+000-576+000 on N-25	222.849	20/5/2021	To be Procured	20/10/2021	178 Days	30.06.2022
9	Km 197+000-200+000 on N-40	83.158	20/5/2021	To be Procured	20/10/2021	178 Days	30.06.2022
10	Km 737+000-759+000 on N-25	211.771	20/5/2021	To be Procured	20/10/2021	178 Days	30.06.2022
11	Km 220+000-231+000 on N-70	95.311	20/5/2021	To be Procured	20/10/2021	178 Days	30.06.2022
12	Km 210+000-220+000 on N-70	85.64	20/5/2021	To be Procured	20/10/2021	178 Days	30.06.2022
13	Km 250+000-260+000 on N-70	99.164	20/5/2021	To be Procured	20/10/2021	178 Days	30.06.2022
14	Km 260+000 -280+000 on N-70	113.303	20/5/2021	To be Procured	20/10/2021	178 Days	30.06.2022
15	Km 290+000-308+000 on N-70	99.449	20/5/2021	To be Procured	20/10/2021	178 Days	30.06.2022
16	KM 566+00 KM 576+00 on N-25	12.8	20/5/2021	To be Procured	20/10/2021	178 Days	30.06.2022
17	KM 601+00 – 616+00 on N-25	49.413	20/5/2021	To be Procured	20/10/2021	178 Days	30.06.2022

Balochistan – South (2017-18)

Sr No	Route	Location		Contractor	Completion Date	Cost	Progress
		From	To				
1	N-25	471.000	477.000	M/s Taj & Brothers	02.01.2021	55,996,666	100%
2	N-25	23.950	27.000	M/s Zarak Construction Company	20.05.2020	105,800,425	100%

Balochistan South (2018-19)

Sr. No.	Route	Engr Est	Location		Contractor Name	Contract Cost	Completion Date	Progress
			To	From				
1	N-25	228.398	410+00	430+00	M/s Saifullah Mohammad Shahi	128.725	-	Under Award
2	N-25	137.194	82+00	96+00	M/s AA Memon	81.768	14.11.2021	5%
3	N-25	378.710	181+00	194+00	M/s QaimKhani & Bros.	226.488	03.10.2021	5%
4	N-25	466.104	194+00	210+00	M/s QaimKhani & Bros.	478.476	03.01.2021	5%
5	N-25	280.992	480+00	500+00	M/s NK & Company	174.662	07.12.2021	5%
6	N-25	114.409	291+00	292+800	M/s Hafeezullah Lehri	76.539	3.11.2021	5%

Baluchistan South (2019-20)

Sr No	Scheme	Engineer's Estimate	T.S Date	Procurement Status		Award Date (Expected)	Completion Time	Completion Date (Expected)
				TBER Status	PBER Status			
1	N-25, 22+00 -23+00 & 32+00 - 34+00, 35+00 - 40+00 & 43+00 - 45+00	130.361	3/12/2020	Under Process	Under Process	Aug-21	178 Days	Feb-2022
2	N-25, 540+00 - 545+00	83.330	5/11/2020	Approved	Under Process	Aug-21	178 Days	Feb-2022
3	N25, 210+00 - 215+00	65.181	5/11/2020	Approved	Under Process	Aug-21	178 Days	Feb-2022
4	N25, 217+00 - 222+00	65.181	5/11/2020	Approved	Under Process	Aug-21	178 Days	Feb-2022
5	N-25 - 45+00 -47+00	74.340	5/11/2020	Approved	Under Process	Aug-21	178 Days	Feb-2022
6	N-25 - 515+00 - 530+00	349.680	3/12/2020	Under Process	Under Process	Aug-21	178 Days	Feb-2022
7	N-25 - 400+00 - 410+00 -	284.870	3/12/2020	Under Process	Under Process	Aug-21	178 Days	Feb-2022

Balochistan South (2020-21)

Sr No	Scheme	Eng Est (Million)	T.S Date (Expected)	Procurement Status	Award Date (Expected)	Completion Time	Completion Date (Expected)
1	Km 126+000-154+000 on M-8	183.344	20/5/2021	To be Procured	20/10/2021	178 Days	30.06.2022
2	Km 154+000-183+000 on M-8	244.101	20/5/2021	To be Procured	20/10/2021	178 Days	30.06.2022
3	Km 477+000 - 480+000 on N-25	84.184	20/5/2021	To be Procured	20/10/2021	178 Days	30.06.2022
4	96+000-105+000 on N-25	117.018	20/5/2021	To be Procured	20/10/2021	178 Days	30.06.2022
5	Km 25+700-28+000 on N-25	41.932	20/5/2021	To be Procured	20/10/2021	178 Days	30.06.2022
6	39+000-47+000 on N-85	188.765	20/5/2021	To be Procured	20/10/2021	178 Days	30.06.2022
7	460+000-470+000 on N-25	287.457	20/5/2021	To be Procured	20/10/2021	178 Days	30.06.2022
8	365+000-373+000 on N-25	216.06	20/5/2021	To be Procured	20/10/2021	178 Days	30.06.2022
9	330+000-345+000 on N-25	270.053	20/5/2021	To be Procured	20/10/2021	178 Days	30.06.2022

Balochistan – West (2017-18)

Sr No	Route	Location		Contractor	Completion Date	Cost	Progress
		From	To				
1	N-10	23.000 42.000	28.000 50.000	M/s Haji Abdul Karim Badini	09.08.2020	87.012	10%
2	N-10	242.000 255.000	244.000 260.000	M/s Karamullah	08.02.2021	64.726	30%
3	N-10	443	452	M/s RMC Cont. Co. JV M/s HRK & Co.	09.08.2020	87.012	10% Case for Re-location in process

Balochistan West (2018-19)

Sr. No.	Route	Engr Est	Location		Contractor Name	Contract Cost	Completion Date	Progress
			To	From				
2	N-10	160.462	213+00 260+00	218+00 268+00	M/s Nawaz Engineer & Azeem Shah	106.274	25.08.2021	80%
3	N-10	118.162	218+00	228+00	M/s Nawaz Engineer & Azeem Shah	78.259	25.08.2021	80%
4	N-10	120.624	228+00	238+00	M/s Nawaz Engineer & Azeem Shah	79.889	25.08.2021	80%
5	N-10	129.376	270+00	317+00	M/s King Enterprise & M.Umar Baloch	93.641	12.06.2021	10%
6	N-10	37.068	344+00	347+00	M/s Muhammad Umer Baloch	24.650	12.12.2020	100%
7	N-10	142.785	425+00	444+00	M/s King Enterprise & M.Umar Baloch	92.310	12.06.2021	65%

Baluchistan West (2019-20)

Sr No	Scheme	Engineer's Estimate	T.S Date	Procurement Status		Award Date (Expected)	Completion Time	Completion Date (Expected)
				TBER Status	PBER Status			
2	N-10 - Km 60+00 - 65+00 & Km 80+00-85+00	133.557	3/12/2020	Under Process	Under Process	Aug-21	178 Days	Feb-2022
3	N-10 - Km 250+00 - 260+00	142.468	3/12/2020	Under Process	Under Process	Aug-21	178 Days	Feb-2022
4	N-10 - Km 270+00 - 350+00	228.277	3/12/2020	Under Process	Under Process	Aug-21	178 Days	Feb-2022
5	N-10 - Km 400+00 - 440+00	220.668	3/12/2020	Under Process	Under Process	Aug-21	178 Days	Feb-2022

Balochistan West (2020-21)

1	KM 247+00 – KM 250+00 on N-10	32.28	20/5/2021	To be Procured	20/10/2021	178 Days	30.06.2022
2	KM 210+00 -213+00, 238+00 - 242+00 & 244+00 - 247+00 on N-10	105.84	20/5/2021	To be Procured	20/10/2021	178 Days	30.06.2022
3	KM 42+00-50+00 on N-10	92.688	20/5/2021	To be Procured	20/10/2021	178 Days	30.06.2022
4	Km 350+00 - 378+00 on N-10	215.118	20/5/2021	To be Procured	20/10/2021	178 Days	30.06.2022
5	433+00 – 442+00	87.012	20/5/2021	To be Procured	20/10/2021	178 Days	30.06.2022
