




GOVERNMENT OF PAKISTAN
MINISTRY OF COMMUNICATIONS
NATIONAL HIGHWAY AUTHORITY




**Procurement Status of Annual Maintenance Plans
2017-18, 2018-19 , 2019-20 & 2020-21**

As on 13th July 2021



Details of Works under AMP 2017-18, 2018-19, 2019-20 and 2020-21

Maintenance of NHA Network South Zone (Sindh Province)



BALUCHISTAN


INDIA

Legend


- ★ Provincial Capital
- City/Town
- National Highway/Strategic Road
- Motorway (Operational)
- Sindh North
- Sindh South
- ▭ Provincial Boundary

Legend

- AMP 2020-21
- AMP 2019-20
- AMP 2018-19
- AMP 2017-18

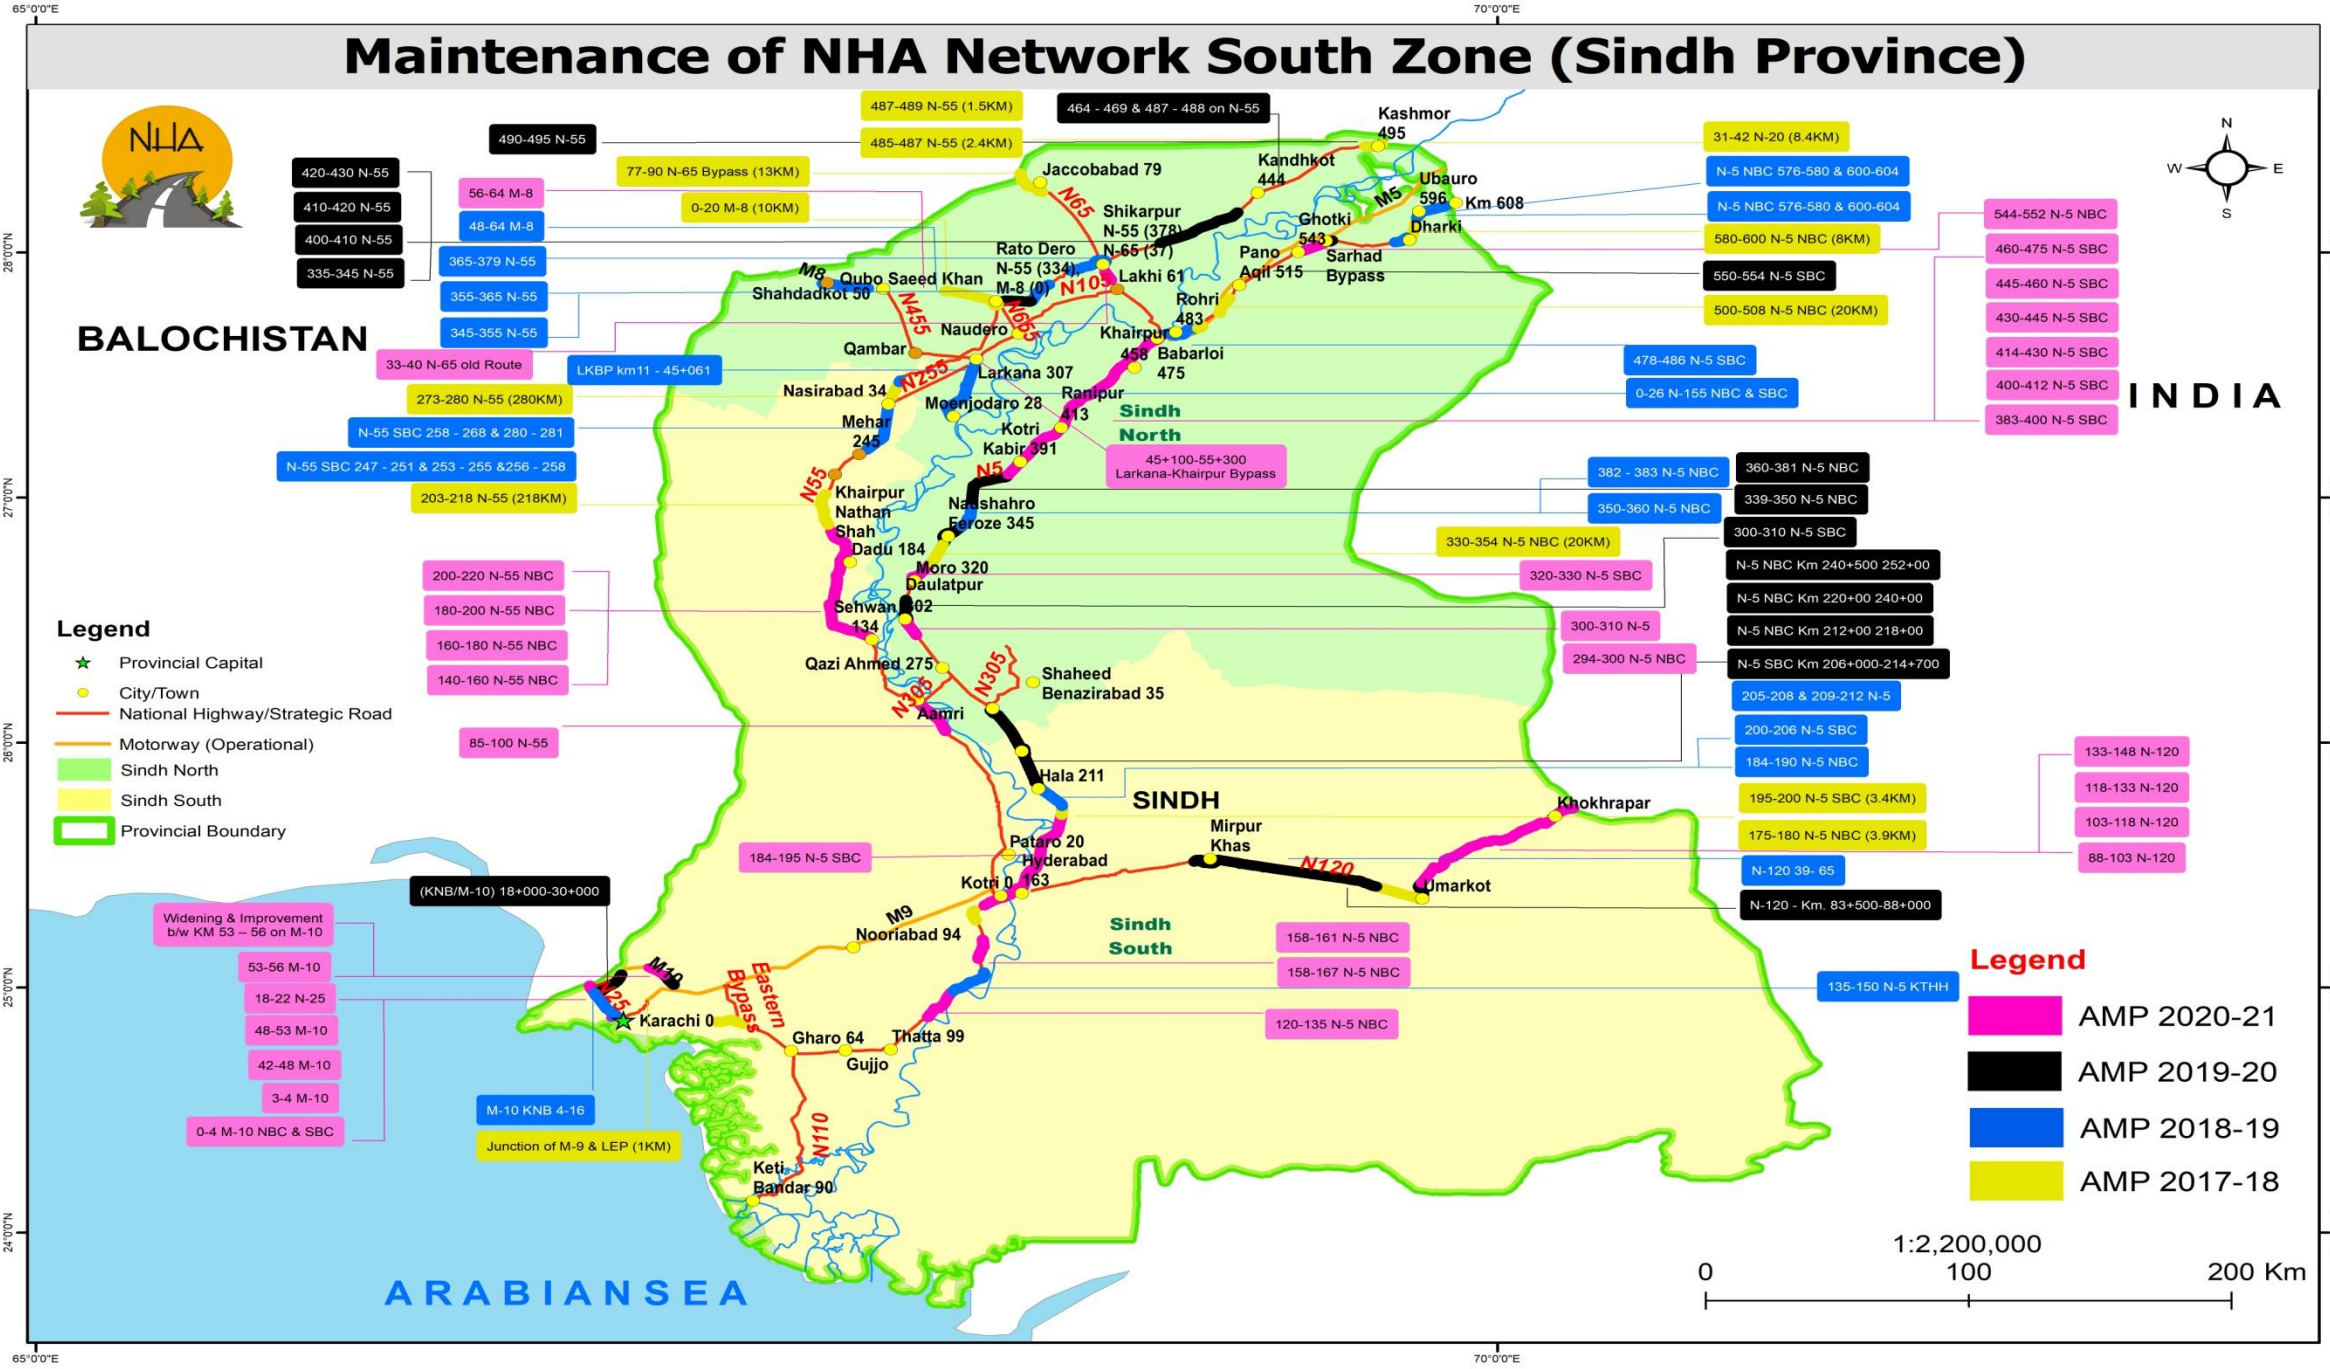

1:2,200,000



Sindh – North (2017-18)

Sr No	Route	Location		Contractor	Completion Date	Cost	Progress
		From	To				
1	N-5 NBC	500.000	508.000	M/s Umer Jan & Co.	02.08.2020	137,343,488	100%
2	N-5 NBC	580.000	600.000	M/s King Enterprises - Mustafa Enterprises (JV)	16.08.2020	289,515,376	100%
3	N-5 SBC	330.000	354.000	M/s King Enterprises - Mustafa Enterprises (JV)	15.05.2020	275,481,893	100%
4	N-20	31.000	42.000	M/s HRK - Jhalawan (JV)	28.01.2021	194,719,074	100%
5	N-55	485.000	487.800	M/s MAC Engineer's & Co.	02.04.2020	53,345,726	100%
6	N-65 (Bypass)	77.000	90.000	M/s HRK & Co.	02.01.2021	220,168,821	100%
7	M-8	0.000	20.000	M/s Mir Ahmed Jan Bangulzai	16.08.2020	172,341,569	100%
8	N-55 NBC	487.800	489.300	M/s Zahir Enterprises	25.08.2020	31,207,369	100%

Sindh North (2018-19)

Sr No	Scheme	Engr Est	Location		Name of Contractor	Completion Time	Contract Cost	Progress
			From	To				
1	N-155 NBC	244.148	0	26	Under Award Process	178 Days	-	Under Award Process
2	N-155 SBC	220.271	0	26	Under Award Process	178 Days	-	Under Award Process
3	N-5 NBC	182.757	576 600	580 604	M/s Nauman Construction Co.	18.02.2021	116.836	88%
4	N-5 SBC	202.696	478	486	M/s A.A Memon	11.07.2021	127.698	10%
5	N-5 SBC	292.758	590	603	M/s Nazir Construction Co.	08.07.2021	184.438	80%
6	N-5 NBC	117.169	350	360	M/s A.A Memon	17.02.2021	74.988	100%
7	N-55	206.799	365	379	Under Award Process	178 Days	-	Under Award Process
8	N-55	176.685	345	355	Under Award Process	178 Days	-	Under Award Process
9	N-55	167.651	355	365	Under Award Process	178 Days	-	Under Award Process
10	M-8	225.391	48	64	M/s Nazir Cosntruction Co.	25.05.2021	141.996	20%
11	LKBP	210.658	11	45+061	Under Award Process	178 Days	-	Under Award Process
12	N-5 NBC	99.987	382	383	M/s Zahid Ali Jatoi	01.04.2021	74.440	100%

Sindh North (2019-20)

Sr No	Scheme	Engineer's Estimate	T.S Date	Procurement Status		Award Date (Expected)	Completion Time	Completion Date (Expected)
				TBER Status	PBER Status			
1	KM 300+00 - 310+00 (SBC) on N-5	79.144	5/11/2020	Approved	Under Award	Aug-21	178 Days	Feb -22
2	339+00 - 350+00 (NBC) on N-5	152.240	3/12/2020	Approved	Under Award	Aug-21	178 Days	Under Award
3	360+00 - 381+00 (NBC) on N-5	393.149	3/12/2020	Approved	Under Award	Aug-21	178 Days	Under Award
4	335+00 - 345+00 on N-55	203.562	3/12/2020	Approved	Under Award	Aug-21	178 Days	Under Award
5	400+00 - 410+00 on N-55	273.199	3/12/2020	Approved	Under Award	Aug-21	178 Days	Under Award
6	410+00 - 420+00 on N-55	284.654	3/12/2020	Approved	Under Award	Aug-21	178 Days	Under Award
7	420+00 - 430+00 on N-55	283.567	3/12/2020	Approved	Under Award	Aug-21	178 Days	Under Award
8	490+00 - 495+00 on N-55	161.010	3/12/2020	Approved	Under Award	Aug-21	178 Days	Under Award
9	550+00 - 554+00 (SBC) on N-5	88.977	5/11/2020	Approved	Under Award	Aug-21	178 Days	Under Award
10	464+700 - 469+00 & 487+000 - 488+000 on N-55	163.661	3/12/2020	Approved	Under Award	Aug-21	178 Days	Under Award

Sindh North (2020-21)

Sr No	Scheme	Eng Est (Million)	T.S Date (Expected)	Procurement Status	Award Date (Expected)	Completion Time	Completion Date (Expected)
1	Km 294+00 - 300+00 (NBC) on N-5	182.946	20/5/2021	To be Procured	October 2021	178 Days	30.06.2022
2	Km 320+000-330+000 (SBC) on N-5	301.835	20/5/2021	To be Procured	October 2021	178 Days	30.06.2022
3	Km 383+00-400+00 (SBC) on N-5	303.133	20/5/2021	To be Procured	October 2021	178 Days	30.06.2022
4	KM 400+00 - 412+00 (SBC) N-5	303.13	20/5/2021	To be Procured	October 2021	178 Days	30.06.2022
5	Km 414+00-430+00 (SBC) on N-5	382.274	20/5/2021	To be Procured	October 2021	178 Days	30.06.2022
6	Km 430+00-445+00 (SBC) on N-5	396.416	20/5/2021	To be Procured	October 2021	178 Days	30.06.2022
7	Km 445+00-460+00 (SBC) on N-5	353.991	20/5/2021	To be Procured	October 2021	178 Days	30.06.2022
8	Km 460+00-475+00 (SBC) on N-5	339.848	20/5/2021	To be Procured	October 2021	178 Days	30.06.2022
9	km 45+100-55+300	286.383	20/5/2021	To be Procured	October 2021	178 Days	30.06.2022
10	Km 544+00-552+00 (NBC) on N-5	231.079	20/5/2021	To be Procured	October 2021	178 Days	30.06.2022
11	Km 33+00-40+00 on N-65 (Old Route)	125.473	20/5/2021	To be Procured	October 2021	178 Days	30.06.2022
12	KM56+00 - 64+00 on M-8	150	20/5/2021	To be Procured	October 2021	178 Days	30.06.2022
13	KM 300+000-310+00 on N-5	79.19	20/5/2021	To be Procured	October 2021	178 Days	30.06.2022

Sindh-South (2017-18)

Sr No	Route	Location		Contractor	Completion Date	Cost	Progress
		From	To				
1	N-5 KTHH NBC	34+00	44+00	NOC issued to local Government			
2	N-5 SBC	195+00	200+00	M/s Insaf & Brothers	25.03.2020	55,656,535	100%
3	N-55	203+00	218+00	M/s. Shaikh Iqbal Akhtar & co.	17.09.2020	254,040,519	100%
4	N-55	273+00	280+00	M/s Zahid Ali Jatoi	05.06.2020	105,010,257	100%
7	N-120	65+00	82+00	M/s Jan Brothers JV GTE	13.01.2022	294,410,000	30%

Sindh South (2018-19)

Sr No.	Scheme	Engr Est	Location		Contractor Name	Contract Cost	Completion date	Progress
			From	To				
1	N-5 KTHH	222.004	135+00	150+00	Under Award	-	178 Days	Under Award Process
2	M-10 (KNB)	132.885	4+00	16+00	M/s Kaim Khani & Brothers	73.207	178 Days	Commencement delayed on request of Sindh Govt.
3	N-5 NBC	116.209	184+00	190+00	M/s Kaim Khani & Brothers	71.538	01.09.2021	20%
4	N-5 SBC	116.409	200+00	206+00	M/s Kaim Khani & Brothers	116.409	01.09.2021	Case at HQ for correction in location
5	N-5 NBC	135.610	205+860 209+640	208+00 212+00	M/s Kaim Khani & Brothers	83.957	01.09.2021	25%
6	N-55 SBC	218.719	247+00 253+00 256+00	251+00 255+00 258+00	M/s Friends Enterprises	119.20	06.10.2021	15%
7	N-55 SBC	292.902	258 280	268 281	M/s Friends Enterprises	166.222	06.10.2021	15%
8	N-120	644.436	39	65	M/s Fazal & Brothers	515.936	01.09.2021	12%

Sindh South (2019-20)

Sr No	Scheme	Engineer's Estimate	Location		Contractor Name	Contract Cost	Completion Date	Progress
			From	To				
1	(KNB/M-10) 18+000-30+000	141.539	18	30	M/s Insaf & Brothers	82.758	27.06.2022	In Mobilization Stage
2	N-5 SBC Km 206+000-214+700	139.641	Sections Shifted in Chinese Grant & revalidation of revised Allocation in AMP 2020-21				178 Days	
3	N-5 NBC Km 212+00-218+00	234.910					178 Days	
4	N-5 NBC Km 220+00-240+00	782.465					178 Days	
5	N-5 NBC Km 240+500-252+00	450.209					178 Days	
6	N-120 - Km. 83+500-88+000	175.330					83+500	88+00

Sindh South (2020-21)

Sr No	Scheme	Eng Est (Million)	T.S Date (Expected)	Procurement Status	Award Date (Expected)	Completion Time	Completion Date (Expected)
1	Km 02+700-04+000 (NBC) & 0+000-4+000 (SBC) on KNB/M-10	49.967	20/5/2021	To be Procured	20/10/2021	178 Days	30.06.2022
2	Km 140+000-160+000 (NBC) on N-55	120.524	20/5/2021	To be Procured	20/10/2021	178 Days	30.06.2022
3	Km160+000+180+000 (NBC) on N-55	126.223	20/5/2021	To be Procured	20/10/2021	178 Days	30.06.2022
4	Km 85+00-100+00 (Old Carriageway) on N-55	111.961	20/5/2021	To be Procured	20/10/2021	178 Days	30.06.2022
5	Km 180+00-200+00 (NBC)on N-55	160.271	20/5/2021	To be Procured	20/10/2021	178 Days	30.06.2022
6	Km 200+00-220+00 (NBC)on N-55	71.662	20/5/2021	To be Procured	20/10/2021	178 Days	30.06.2022
7	Km 53+200-56+000 on KNB/M-10	340.226	20/5/2021	To be Procured	20/10/2021	178 Days	30.06.2022
8	N-5 NBC Km 120+000-135+000	231.804	20/5/2021	To be Procured	20/10/2021	178 Days	30.06.2022
9	N-5 NBC Km 158+000-167+000	77.818	20/5/2021	To be Procured	20/10/2021	178 Days	30.06.2022
10	N-5 SBC Km 158+500-161+920	279.594	20/5/2021	To be Procured	20/10/2021	178 Days	30.06.2022
11	N-5 SBC Km 184+257-195+000	267.469	20/5/2021	To be Procured	20/10/2021	178 Days	30.06.2022
12	N-120 Km 88+000-103+000	288.144	20/5/2021	To be Procured	20/10/2021	178 Days	30.06.2022
13	N-120 Km 103+000-118+000	292.902	20/5/2021	To be Procured	20/10/2021	178 Days	30.06.2022
14	Widening & Improvement b/w KM 53+00 – 56+00 on M-10	270.5	20/5/2021	To be Procured	20/10/2021	178 Days	30.06.2022
15	KM 42+620 – KM 48+00 on (KNB/M10)	156	20/5/2021	To be Procured	20/10/2021	178 Days	30.06.2022
16	KM 48+00 – KM 53+00 on (KNB/M10)	156	20/5/2021	To be Procured	20/10/2021	178 Days	30.06.2022
17	KM 18+700 – 22+00 on N-25	358.606	20/5/2021	To be Procured	20/10/2021	178 Days	30.06.2022
	KM 118+00 – KM 123+00 on N						
