




GOVERNMENT OF PAKISTAN
MINISTRY OF COMMUNICATIONS
NATIONAL HIGHWAY AUTHORITY




**Procurement Status of Annual Maintenance Plans
2017-18, 2018-19 , 2019-20 & 2020-21**

As on 13th July 2021




Details of Works under AMP 2017-18, 2018-19, 2019-20 and 2020-21

Maintenance of NHA Network Central Zone (Punjab Province)

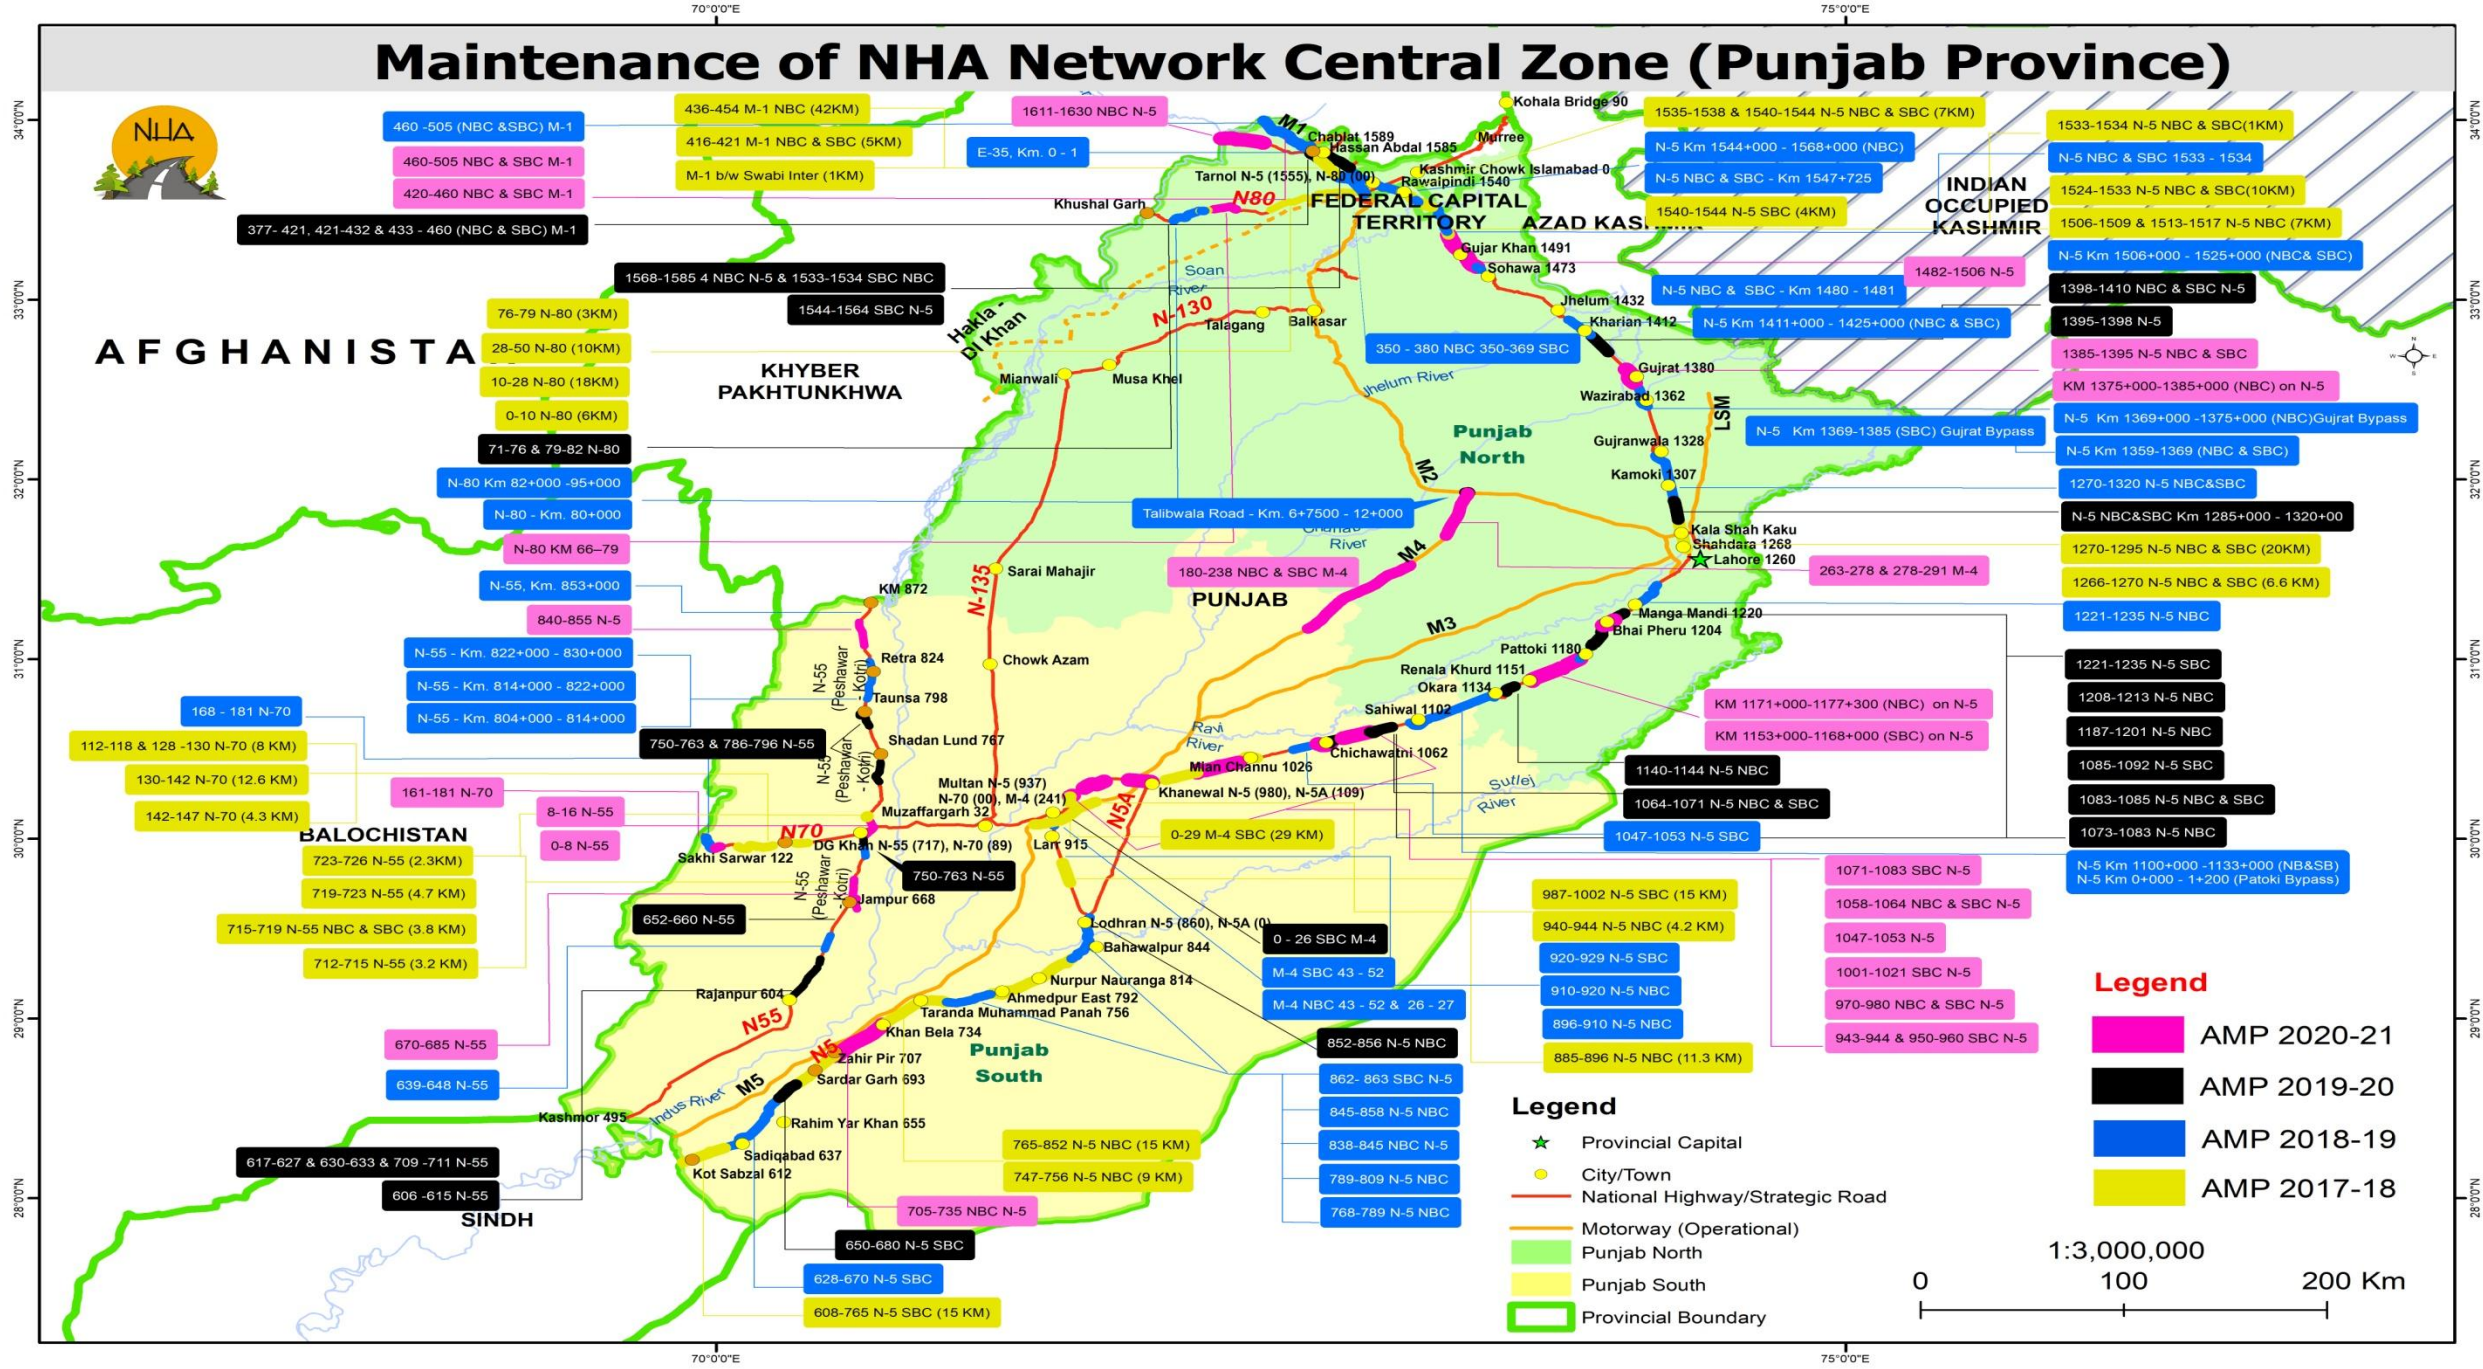

- Legend**
- ★ Provincial Capital
 - City/Town
 - National Highway/Strategic Road
 - Motorway (Operational)
 - Punjab North
 - Punjab South
 - Provincial Boundary

- Legend**
- AMP 2020-21
 - AMP 2019-20
 - AMP 2018-19
 - AMP 2017-18



Punjab North (2017-18)

Sr No	Route	Location		Contractor	Completion Date	Cost	Progress
		From	To				
1	N-5 NBC & SBC	1266.700	1270.000	M/s Allied Constructors	19.07.2019	63,740,000	100%
2	N-5 NBC & SBC	1270.000	1295.000	M/s Taimour Shah	02.11.2019	175,111,122	100%
3	N-5 SBC	1540.000	1544.000	M/s Mughal Construction Co.	120 Days	30,910,000	90%
4	N-5 NBC	1506.000 1513.000	1509.000 1517.000	M/s M. Khawaj Abbasi	27.06.2019	57,541,384	90%
5	N-5 NBC	1535.000 1540.000	1538.000 1544.000	M/s M. Khawaj Abbasi	24.06.2019	57,541,384	72%
6	N-80	10.000	28.000	M/s Khwaj Abbasi	09.11.19	158,315,801	97%
7	N-80	28.000	50.000	M/s MKA & IR JV	09.11.19	82,201,199	100%
8	N-80	76.000	79.000	M/s Taimour Shah	14.11.2020	65,575,000	88%
9	N-80	0.000	10.000	M/s Taimoor Shah Const. Co.	09.09.2019	94,674,636	94%
10	N-5 NBC & SBC	1533.000	1534.000	AK Communications	22.05.2019	1,243,516,168	41%
11	N-5 NB & SB	1524.450	1533.800	M/s Global Technical Enterprises	28.02.2017	1,033,145,000	100%

Punjab North (2018-19)

Sr No	Route	Engr Est	Location		Name of Contractor	Contract Cost	Date of Completion	Progress
			From	To				
1	N-5 NBC&SBC	250.000	1295+00	1325+00	M/s Nauman Construction Co- M/s Talha Const Co JV	147.225	17.09.2021	Not Mobilized yet
2	N-5 (NBC)Gujrat Bypass	49.843	1369+00	1375+00	M/s Indus ACE Engineer	34.170	19.07.2021	92%
3	N-5	140.226	0+800	8+500	M/s Allied Construction Co	86.799	21.10.2021	Contractor Mobilized
4	N-5 Km (NB&SB) N-5 Km 0+000 - 1+200 (Patoki Bypass)	296.421	1100+00 0+00	1133+00 1+200		187.723	178 Days	Not Mobilized yet
5	N-5 NBC Km 1221+500 - 1235+000	168.332	1221+500	1235+00		110.257	178 Days	
6	N-5 (NBC)	129.821	1411+00	1425+00	M/s CKG	81.787	22.06.2021	100%
7	N-5 Km (SBC)	153.690	1411+00	1425+00	M/s CKG	99.683	22.06.2021	100%
8	N-5 Km 1506+000 - 1525+000 (NBC&SBC)	180.865	1506+00	1525+00		103.925	178 Days	
9	N-5 Km (NBC)	297.988	1544+00	1568+00	M/s Nauman Const Co JV M/s Nazir Associates	173.876	17.09.2021	25%
10	N-5 Km (NBC)	198.644	1359+00	1369+00		160.163	178 Days	
11	N-5 Km (SBC)	225.582	1359+00	1369+00		139.051	178 Days	
12	N-5 Km (SBC) Gujrat Bypass	358.964	1369+00	1385+00		265.633	178 Days	
13	N-80	350.835	82+00	95+00	M/s HRK & Co	263.880	12.01.2021	95%
14	N-80 - Km. 80+000	36.750	80+00	80+00	-	-		-
15	N-5 NBC & SBC - Km 1547+725	123.000	1547+725	1547+725	-	-	-	-
16	N-5 NBC & SBC - Km 1533 - 1534 – Phase-II	198.644	1533+00- 1534+00		M/s A.K.Communications	1412.00	30.12.2021	42%
17	N-5 NBC & SBC - Km 1480 - 1481	225.440	Improvement of Curve (Under Design Phase)		-	-	-	Under Design

Punjab North (2019-20)

Sr No	Scheme	Engineer's Estimate	T.S Date	Procurement Status		Award Date	Completion Date	Contract Cost	Progress
				TBER Status	PBER Status				
1	N-5 NBC&SBC Km 1285+000 - 1320+00	247.137	3/12/2020	Finalized	Awarded to M/s Dughal & Co	01.07.2021	29.01.2022	145.540	Under Mobilization
2	1187+00 - 1201+300 (NBC) on N-5	338.157	3/12/2020	Finalized	Awarded to M/s Fast Track & Co	17.06.2021	13.12.2021	270.530	Mobilized at Site
3	00+99 - 07+100 (Phoolnagar Bypass) & 1208+00 - 1213+00 (NBC) on N-5	298.570	3/12/2020	Finalized	Awarded to M/s Ugalco	29.06.2021	30.12.2021	238.170	Letter of Commencement issued
4	1221+500 - 1235+00 (SBC) on N-5	329.690	3/12/2020	Finalized	Awarded to M/s Fast Track & Co	17.06.2021	13.12.2021	267.050	Mobilized at Site
5	1398+400 - 1410+00 (NBC) on N-5	372.960	3/12/2020	Finalized	Awarded to M/s Mughal Const JV M/s Pervaiz Const	Under Award Process	178 Days	232.240	Under Award
6	1398+400 - 1410+00 (SBC) on N-5	372.960	3/12/2020	Finalized	Awarded to M/s Highway Const Co	-do-	178 Days	232.240	-do-
7	1140+700 - 1144+200 (NBC) on N-5	95.260	5/11/2020	Finalized	Awarded to M/s INDUS ACE	Under Process	178 Days	75.160	-do-
8	1544+00 - 1564+250 (SBC) on N-5	350.000	3/12/2020	Finalized	Awarded to M/s Ugalco	29.06.2021	30.12.2021	199.110	Letter of Commencement issued
9	1568+00 - 1585+00 (NBC) on N-5	350.000	3/12/2020	Finalized	Awarded to M/s Ugalco	29.06.2021	30.12.2021	199.150	Letter of Commencement issued
10	1395+800 - 1398+400 (NBC & SBC) on N-5	310.138	3/12/2020	Finalized	Awarded to M/s Mughal Const JV M/s Pervaiz Const	Under Process	178 Days	257.350	Under Award
11	71+00 - 76+00 & 79+00 - 82+00 on N-80	215.650	3/12/2020	Finalized	Awarded to	Aug-21	178 Days	132.708	

Punjab North (2020-21)

Sr No	Scheme	Eng Est (Million)	T.S Date (Expected)	Procurement Status	Award Date (Expected)	Completion Time	Completion Date (Expected)
1	KM 0+000-12+500 (SBC),KM 0+000-2+000(NBC),KM 5+700-12+500 (NBC) on N-5	481.743	20/5/2021	To be Procured	20/10/2021	178 Days	30.06.2022
2	KM 1153+000-1168+000 (SBC) on N-5	260.255	20/5/2021	To be Procured	20/10/2021	178 Days	30.06.2022
3	KM 1171+000-1177+300 (NBC) on N-5	236.981	20/5/2021	To be Procured	20/10/2021	178 Days	30.06.2022
4	KM 0+000-6+000 on N-5	163.365	20/5/2021	To be Procured	20/10/2021	178 Days	30.06.2022
5	KM 0+000-7+500 on N-5	226.23	20/5/2021	To be Procured	20/10/2021	178 Days	30.06.2022
6	KM 1375+000-1385+000 (NBC) on N-5	293.105	20/5/2021	To be Procured	20/10/2021	178 Days	30.06.2022
7	KM 1482+000-1506+000 (NBC) on N-5	265.044	20/5/2021	To be Procured	20/10/2021	178 Days	30.06.2022
8	KM 1385+000-1395+000 (NBC) on N-5	347.299	20/5/2021	To be Procured	20/10/2021	178 Days	30.06.2022
9	KM 1385+000-1395+000 (SBC) on N-5	347.299	20/5/2021	To be Procured	20/10/2021	178 Days	30.06.2022
10	KM 1611+000-1630+000 (NBC) on N-5	492.176	20/5/2021	To be Procured	20/10/2021	178 Days	30.06.2022
11	KM 1611+000-1630+000 (SBC) on N-5	490.526	20/5/2021	To be Procured	20/10/2021	178 Days	30.06.2022
12	N-5S&N - Km 1547+725	523	20/5/2021	To be Procured	20/10/2021	178 Days	30.06.2022
13	N-5 NBC & SBC 1409+850 – 1414+350	199.99	20/5/2021	To be Procured	20/10/2021	178 Days	30.06.2022
14	N-80 KM 66+700 – 79+900	36.75	20/5/2021	To be Procured	20/10/2021	178 Days	30.06.2022

Punjab –South (2017-18)

1	N-5 SBC	987.000	1002.000	M/s InduS ACE Engineers	14.04.20	134,209,293	100%
2	N-5 NBC	608.000	765.000	M/s NCC-NA (JV)	05.11.2019	136,637,819	100%
3	N-5 NBC	765.000	852.000	M/s NCC-NA (JV)	08.11.2019	136,638,261	100%
4	N-5 NBC	747.000	756.000	M/s Sheikh Nazar Muhammad & Co.	11.12.2019	143,426,729	100%
5	N-5 NBC	940.000	944.200	M/s Ugalco Construction Co.	13.07.2019	69,109,067	100%
6	N-5 SBC	1019.000	1030.000	M/s Sh. Iqbal Akhtar & Co.	24.09.2019	177,450,000	100%
7	N-70	112 128	118 130	M/s Allah Dad	28.11.2018	134,447,890	100%
8	N-70	130.000	142.675	M/s Allah Dad	28.11.2018	214,604,166	100%
9	N-70	142.675	147.000	M/s Ugalco Construction Co.	03.08.2018	79,078,056	100%
10	N-55	712.000	715.200	M/s M. Nawaz Engineers	21.05.2018	34,766,212	100%
11	N-55 SBC	715.200	719.000	M/s M. Nawaz Engineers	21.05.2018	37,547,221	100%
12	N-55 NBC	715.200	719.000	M/s M. Nawaz Engineers	21.05.2018	36,491,705	100%
13	N-55	719.000	723.700	M/s M. Nawaz Engineers	21.05.2018	35,773,668	100%
14	N-55	723.700	726.000	M/s Wajid Iqbal & Co	01.05.2018	38,167,275	100%
15	N-5 NBC	885.000	896.300	M/s Muhammad Sajjad	18.09.2019	268,112,000	100%

Punjab South (2018-19)

Sr No	Route	Engr Est	Location		Name of Contractor	Contract Cost	Date of Completion	Progress
			From	To				
1	N-5 SBC	105.259	1047+00	1053+270	Under Award	-	-	-
2	N-5 SBC	311.137	628+00	670+00	M/s Muhammad Sajjad	186.340	17.10.2021	Mobilized at Site
3	N-5 NBC	489.302	768+00	789+00	M/s Wintoss Builders	304.405	9.08.2021	12%
4	N-5 NBC	466.002	789+00	809+00	M/s Wintoss Builders	289.914	09.08.2021	65%
5	N-5 SBC	151.785	920+00	929+00	M/s NCC – NA JV	86.533	04.08.2021	Mobilized at Site
6	N-55	196.199	639+00	648+00	M/s Nauman Const Co	120.329	17.10.2021	Mobilized at Site.
7	N-55	220.542	804+00	814+00	M/s Ugalco	151.953	25.12.2020	100%
8	N-55	220.542	814+00	822+00	M/s Ugalco	151.953	25.12.2020	100%
9	N-55	220.542	822+00	830+00	M/s Ugalco	151.953	25.12.2020	100%
10	N-70	68.059	700+00	707+00	M/s Nawaz Engineers	45.756	16.08.2021	60%
11	N-70	300.950	168+00	181+00	Revalidated under AMP 2020-21			
12	N-55	85.120	853+00	853+00	M/s Rustam Associates	51.937	05.08.2021	50%
13	N-5 SBC	64.100	862+00	863+00	M/s Talha Const	43.654	25.08.2021	44%
14	N-5 NBC	335.171	833+510	845+00	M/s Muhammad Sajjad	191.181	12.10.2021	63%
15	N-5 NBC	376.315	845+00	858+00	M/s Muhammd Sajjad	214.574	12.10.2021	20%


Punjab South (2019-20)

Sr No	Route	Engineer's Estimate	Location		Name of Contractor	Contract Cost	Completion Time	Progress
			From	To				
1	N-5 SBC	138.477	650	680	M/s Mughal Construction Co.	81.147	178 Days	Letter of Commencement issued
2	N-55	232.417	606	615	M/s Ugalco Construction Co.	146.190	178 Days	Letter of Commencement issued
3	N-55	339.819	617 630 709	627 633+625 711	M/s Ugalco Construction Co.	224.715	178 Days	Letter of Commencement issued
4	N-55 NBC	224.184	652	660	M/s Ugalco Construction Co.	141.011	178 Days	Letter of Commencement issued
5	N-55	410.091	750 786	763 796	M/s Mahboobi Associates	255.240	20.12.2021	Just Mobilized
6	N-5 NBC & SBC	444.468	1064	1071+575	M/s King Enterprises JV M/s Mustafa Enterprises	261.747	178 Days	Letter of Commencement issued
7	N-5 NBC & SBC	205.515	1083	1085	M/s Construction Professional Associates	118.705	178 Days	Letter of Commencement issued
8	N-5 NBC	268.879	1073+845	1083	M/s King Enterprises JV M/s Mustafa Enterprises	161.032	178 Days	Letter of Commencement issued
9	N-5 SBC	205.516	1085	1092	M/s Construction Professional Associates	118.676	178 Days	Letter of Commencement issued
10	N-5 NBC	102.237	852+200	856	M/s Wintos Builders	58.623	178 Days	Letter of Commencement issued

Punjab South (2020-21)

Sr No	Scheme	Eng Est (Million)	T.S Date (Expected)	Procurement Status	Award Date (Expected)	Completion Time	Completion Date (Expected)
1	KM 705+00 - 735+00 (NBC) on N-5	455.728	20/5/2021	To be Procured	October 2021	178 Days	30.06.2022
2	KM 943+00-944+00& 950+00-960+00 (SBC) on N-5	347.285	20/5/2021	To be Procured	October 2021	178 Days	30.06.2022
3	KM 1058+00-1064+00 (NBC) on N-5	181.776	20/5/2021	To be Procured	October 2021	178 Days	30.06.2022
4	KM 1058+00-1064+00 (SBC) on N-5	194.015	20/5/2021	To be Procured	October 2021	178 Days	30.06.2022
5	KM 1071+575-1083+400 (SBC) on N-5	379.11	20/5/2021	To be Procured	October 2021	178 Days	30.06.2022
6	KM 970+00-980-00(NBC) on N-5	298.37	20/5/2021	To be Procured	October 2021	178 Days	30.06.2022
7	KM 970+00-980+00 (SBC) N-5	303.36	20/5/2021	To be Procured	October 2021	178 Days	30.06.2022
8	KM 1001+00-1021+00 (SBC) on N-5	593.155	20/5/2021	To be Procured	October 2021	178 Days	30.06.2022
9	KM 670+00-685+00 on N-55	289.097	20/5/2021	To be Procured	October 2021	178 Days	30.06.2022
10	KM 00+000-8+000 on N-55	243.324	20/5/2021	To be Procured	October 2021	178 Days	30.06.2022
11	KM 840+000-855+000 on N-55	396.904	20/5/2021	To be Procured	October 2021	178 Days	30.06.2022
12	KM 8+000-16+000 on N-55	251.348	20/5/2021	To be Procured	October 2021	178 Days	30.06.2022
13	KM 161+00 – 181+00 on N-70	300.95	20/5/2021	To be Procured	October 2021	178 Days	30.06.2022
14	KM 1047+00 - 1053+270	187	20/5/2021	To be Procured	October 2021	178 Days	30.06.2022

Maintenance of NHA Network Central Zone (Punjab Province)

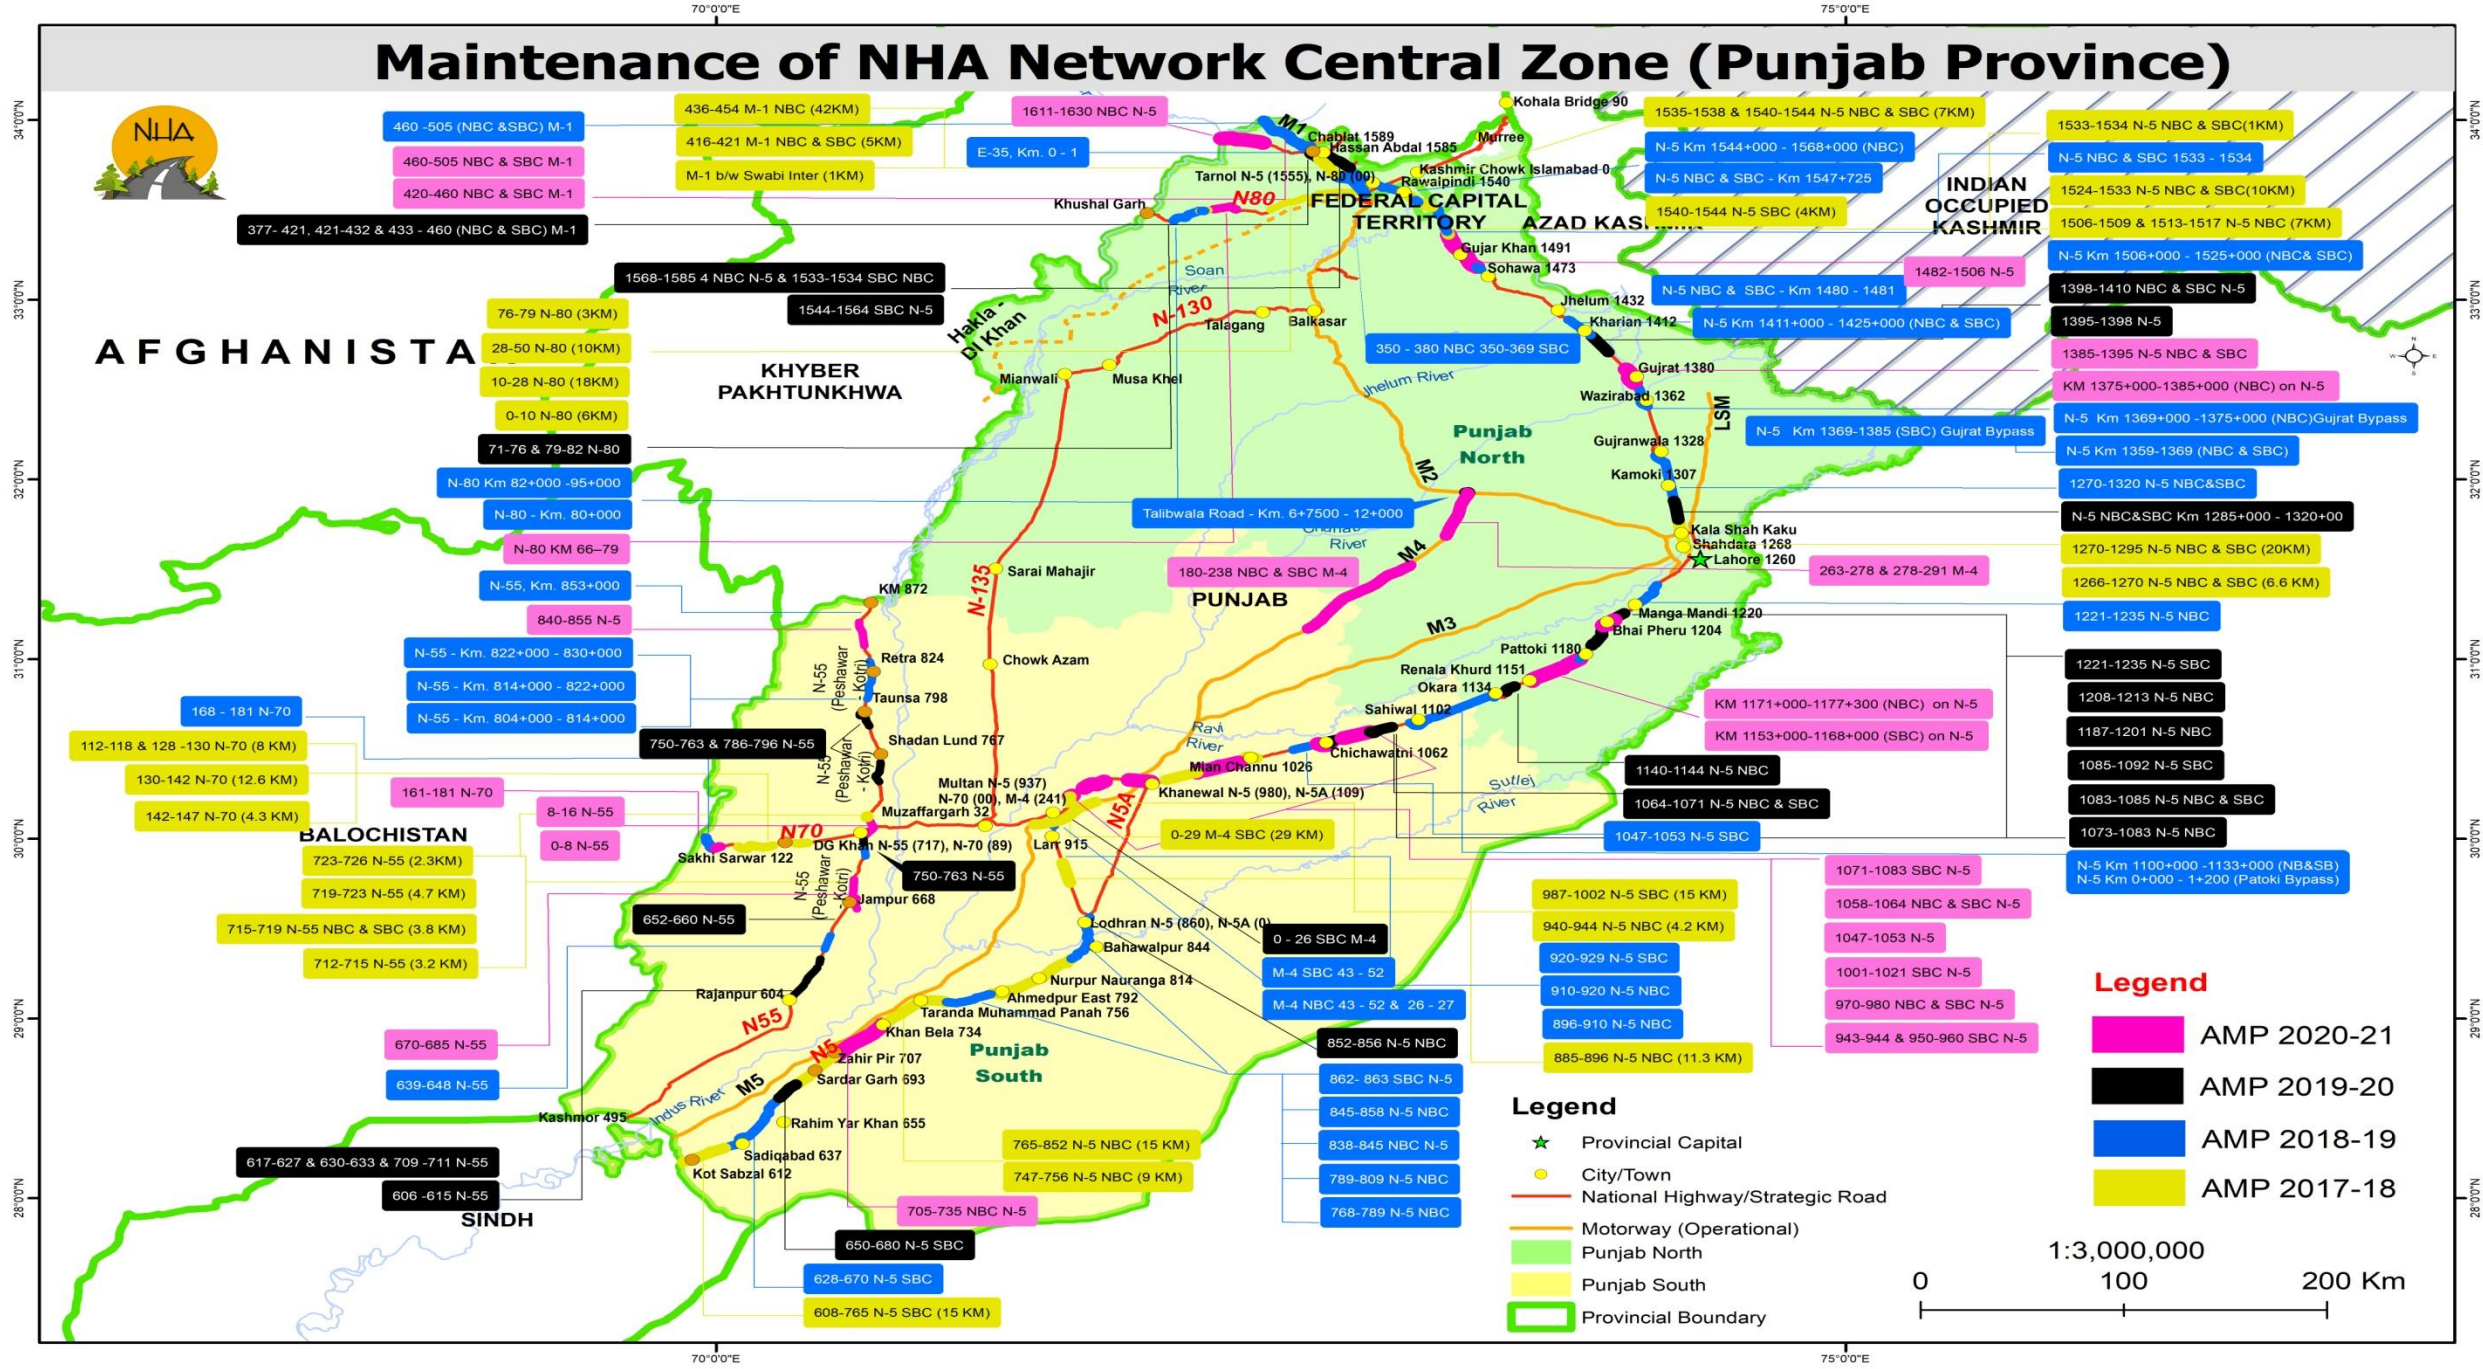

Legend

- AMP 2020-21
- AMP 2019-20
- AMP 2018-19
- AMP 2017-18

Legend

- Provincial Capital
- City/Town
- National Highway/Strategic Road
- Motorway (Operational)
- Punjab North
- Punjab South
- Provincial Boundary

1:3,000,000

0 100 200 Km
