




GOVERNMENT OF PAKISTAN
MINISTRY OF COMMUNICATIONS
NATIONAL HIGHWAY AUTHORITY



**Procurement Status of Annual Maintenance Plans
2017-18, 2018-19 , 2019-20 & 2020-21**

As on 13th July 2021




Details of Works under AMP 2017-18, 2018-19, 2019-20 and 2020-21

Maintenance of NHA Network in North Zone (KPK Province & Gilgit Baltistan)




AFGHANISTAN

CHINA



Legend


- ★ Provincial Capital
- City/Town
- National Highway/Strategic Road
- Motorway (Operational)
- Gilgit - Baltistan
- Khyber Pakhtunkhwa
- Muzaffarabad
- Northern Areas
- Provincial Boundary

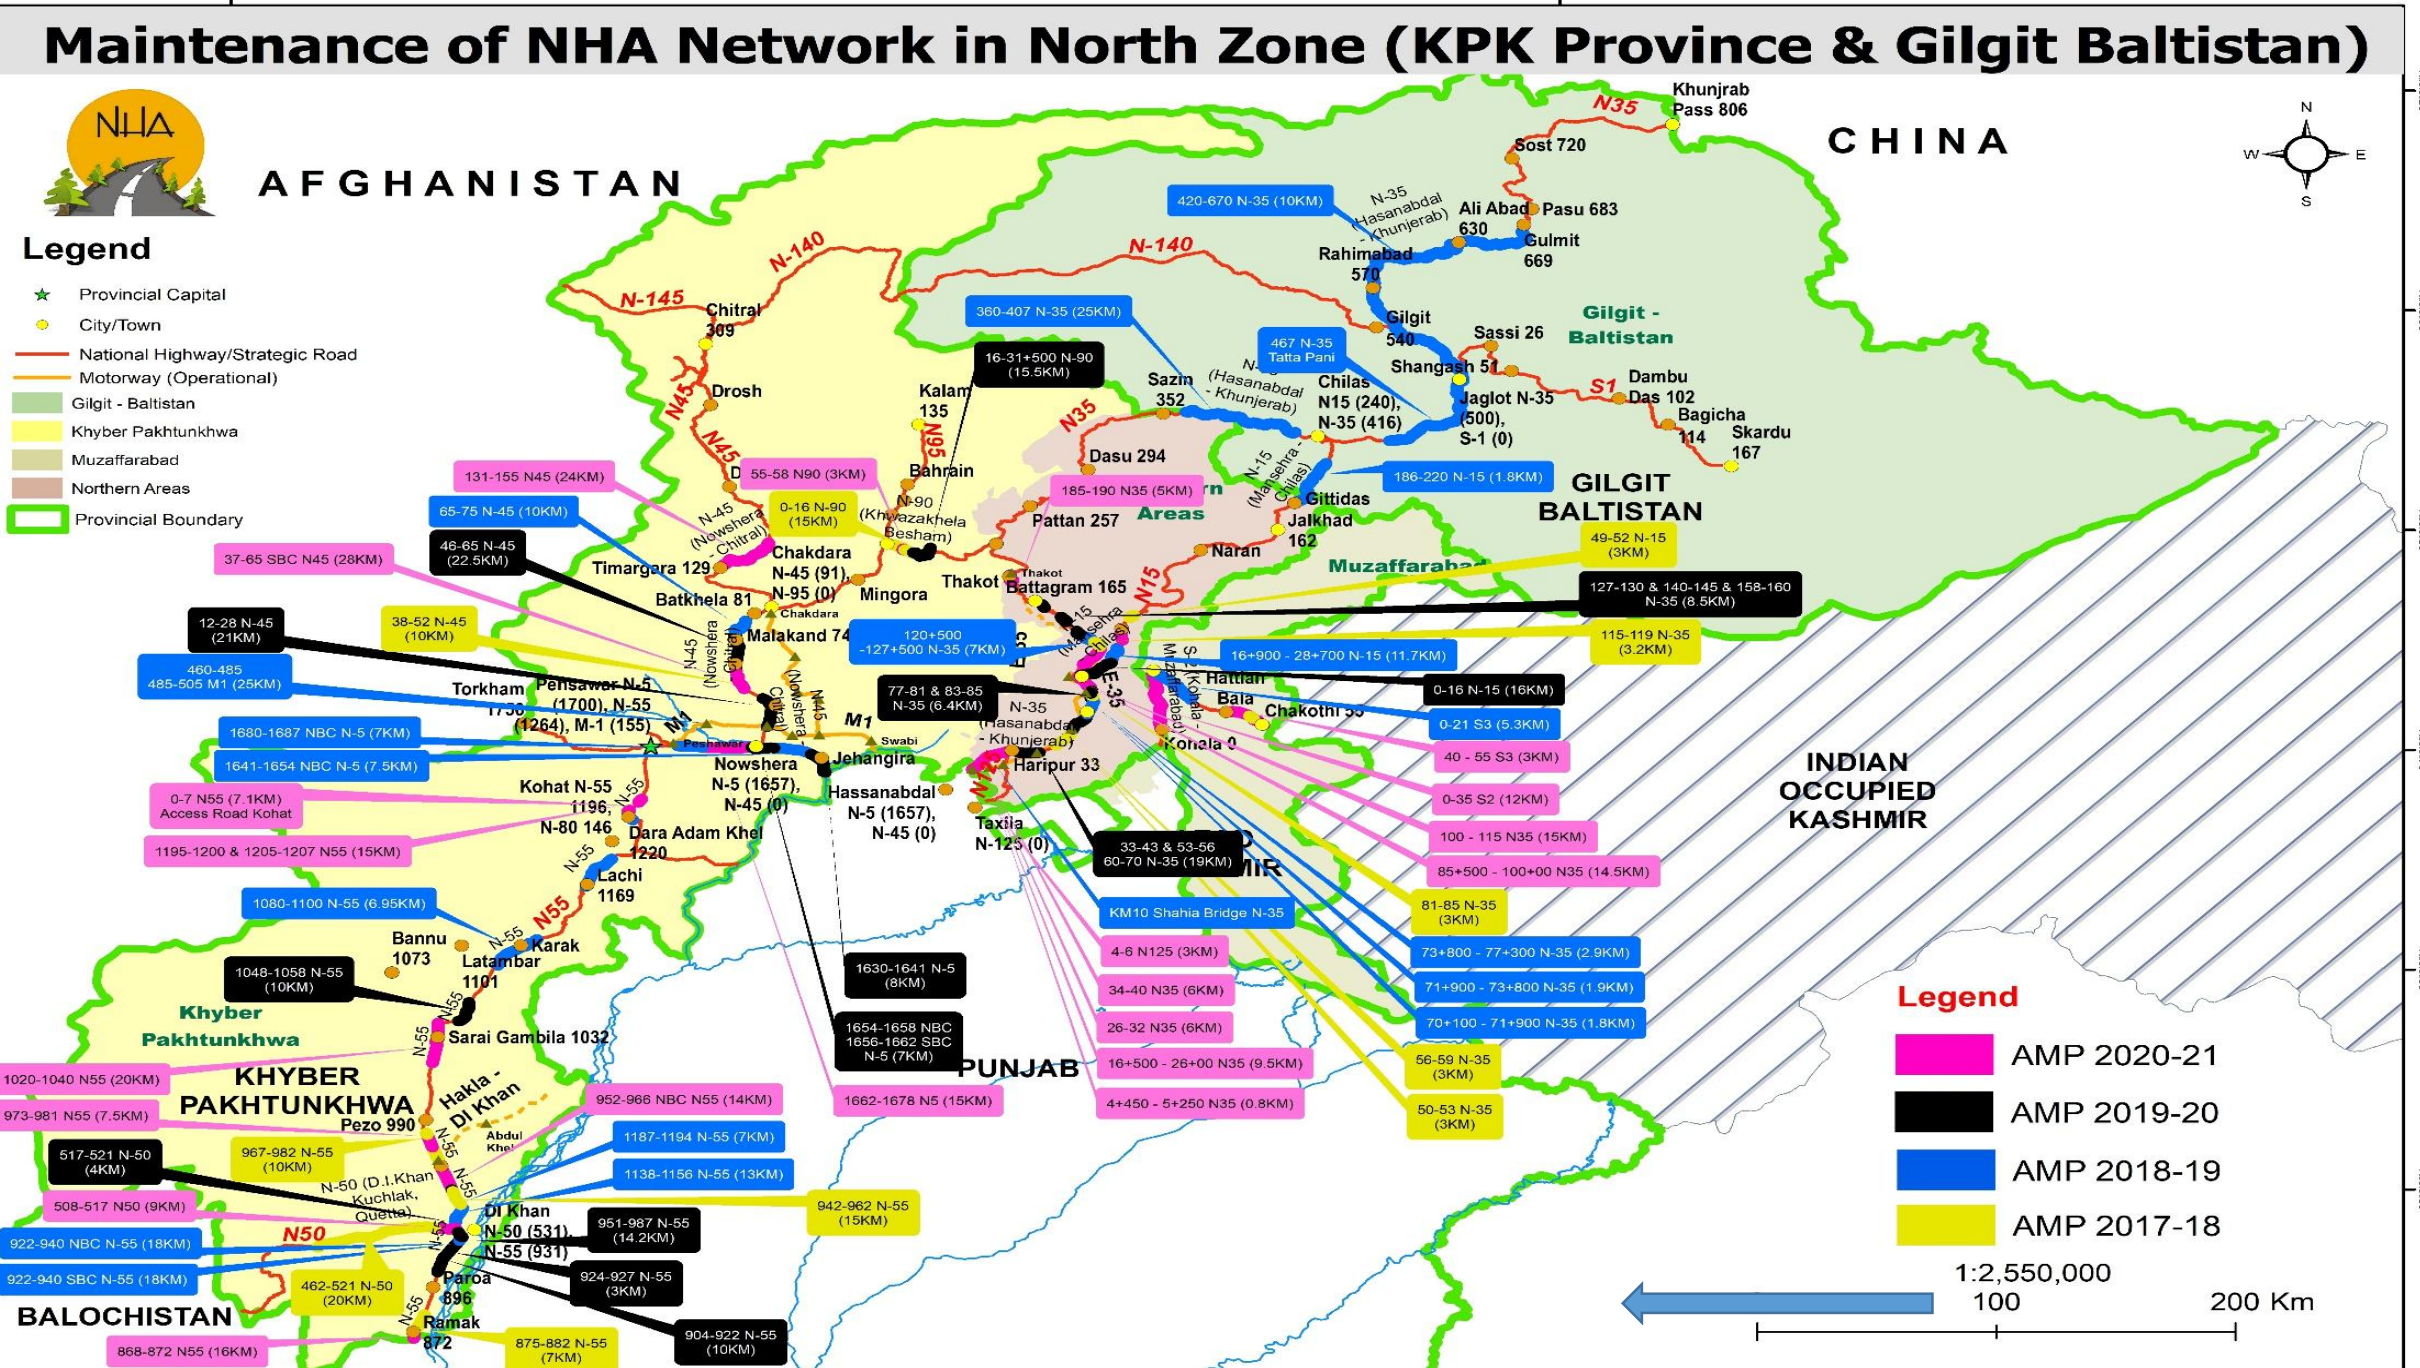

Legend

- AMP 2020-21
- AMP 2019-20
- AMP 2018-19
- AMP 2017-18

1:2,550,000



Khyber Pakhtunkhwa (2017-18)

Sr No	Route	Location		Contractor	Completion Date	Cost	Progress
		From	To				
1	N-45	38.000	52.000	M/S ABDUL HAKEEM & SONS	18.12.2019	154,212,900	100%
2	N-50	462.000	521.000	M/S TAIMOOR SHAH - AL FEROZ JV	18.12.2019	154,964,464	95%
3	N-55 (ACW)	967.000	982.000	M/S MOHMAND CONST LTD	02.02.2021	145,515,636	54%
4	N-55 (ACW)	942.000	962.000	M/S IKAN-NCC JV	02.02.2021	218,188,751	64%
5	N-55	875.000	882.000	M/S MCL- NASRULLAH MINKHEL JV	25.03.2020	103,882,124	Contract Terminated
6	N-90	0.000	16.000	M/S PIR MUHAMMAD - MALAMJABBA JV	17.11.2020	219,820,419	60%

Khyber Pakhtunkhwa (2018-19)

Sr No	Route	Engr Est	Location		Contractor Name	Contract Cost	Completion Date	Progress
			From	To				
1	N-45	165.855	65+00	75+00	M/s Umer Jan & Co. JV M/s Sarwar Khan	103.245	01.12.2021	15%
2	N-55	339.256	1138+00	1156+00	M/s Lawagher Construction Co.	263.874	14.09.2021	10%
3	N-55	240.642	1187+00	1194+00	Under Award	173.262	-	Under Award
4	N-5 NBC	188.603	1680+00	1687+00	M/s Hilton Construction & Engineers (JV) M/s HRK & CO.	126.913	06.10.2021	Under Mobilization
5	N-5 NBC	205.245	1641+00	1654+00	M/s Construction Professional Associates (Pvt) Ltd.	122.900	15.09.2021	24%
6	N-55	170.295	1080+00	1100+00	M/s Lawagher Construction Co.	127.295	14.09.2021	20%
7	N-55 ACW NBC (Bypass)	517.385	922+00	940+00	-	178 Days		

Khyber Pakhtunkhwa (2019-20)

Sr No	Scheme	Engineer's Estimate	T.S Date	Procurement Status		Award Date (Expected)	Completion Time	Completion Date (Expected)
				TBER Status	PBER Status			
1	12+00 - 28+00 (NBC & SBC) on N-45	442.605	3/12/2020	Approved	Under Process	Aug-21	178 Days	Feb-2022
2	46+00 - 65+00 (NBC & SBC) on N-45	474.12	3/12/2020	Under Process	Under Process	Aug-21	178 Days	Feb-2022
3	1630+00 - 1641+00 on N-5	199.974	3/12/2020	Approved	Under Process	Aug-21	178 Days	Feb-2022
4	1654+00 -1658+00 (NBC) 1656+00 -1662+00 (SBC) on N-5	174.228	3/12/2020	Approved	Under Process	Aug-21	178 Days	Feb-2022
5	KM 904+000 - 922+000 on N-55	250.00	3/12/2020	Approved	Under Process	Aug-21	178 Days	Feb-2022
6	16+00 - 31+500 on N-90	225.229	3/12/2020	Under Process	Under Process	Aug-21	178 Days	Feb-2022
7	924+00 - 927+00 on N-55	260.000	3/12/2020	Approved	Approved	LOA issued	178 Days	Feb-2022
8	517+00 - 521+00	187.000	3/12/2020	Approved	Under Process	Aug-21	178 Days	Feb-2022
9	1048+645 - 1058+00 on N-55	293.879	3/12/2020	Approved	Under Process	Aug-21	178 Days	Feb-2022

Khyber Pakhtunkhwa (2020-2021)


Sr No	Scheme	Eng Est (Million)	T.S Date (Expected)	Procurement Status	Award Date (Expected)	Completion Time	Completion Date (Expected)
1	KM 55+000-58+000 on N-90	62.517	20/5/2021	To be Procured	20/10/2021	178 Days	30.06.2022
2	Km 00+000 -7+050 on N-55 Access Road	158.487	20/5/2021	To be Procured	20/10/2021	178 Days	30.06.2022
3	Km 131+000-155+000 on N-45	212.257	20/5/2021	To be Procured	20/10/2021	178 Days	30.06.2022
4	Km 37+00 - 65+00 (SBC) on N-45	402.622	20/5/2021	To be Procured	20/10/2021	178 Days	30.06.2022
5	Km 1662+000-1678+000 on N-5	387.25	20/5/2021	To be Procured	20/10/2021	178 Days	30.06.2022
6	Km 1195+400-1200+750, Km 1205+4000-1207+400 on N-55	593.556	20/5/2021	To be Procured	20/10/2021	178 Days	30.06.2022
7	Km 1020+000-1040+000 on N-55	260.91	20/5/2021	To be Procured	20/10/2021	178 Days	30.06.2022
8	Km 868+000-872+000 on N-55	222.991	20/5/2021	To be Procured	20/10/2021	178 Days	30.06.2022
9	Km 952+000-966+000 on N-55 NBC	396.187	20/5/2021	To be Procured	20/10/2021	178 Days	30.06.2022
10	Km 508+000-517+000 on N-50	103.418	20/5/2021	To be Procured	20/10/2021	178 Days	30.06.2022
11	Km 973+500 -981+00 NBC	212.369	20/5/2021	To be Procured	20/10/2021	178 Days	30.06.2022
12	885+00 – 892+00	166.975	20/5/2021	To be Procured	20/10/2021	178 Days	30.06.2022
Total		3179.539					

Maintenance of NHA Network in North Zone (KPK Province & Gilgit Baltistan)




AFGHANISTAN

CHINA



Legend

- ★ Provincial Capital
- City/Town
- National Highway/Strategic Road
- Motorway (Operational)
- Gilgit - Baltistan
- Khyber Pakhtunkhwa
- Muzaffarabad
- Northern Areas
- Provincial Boundary

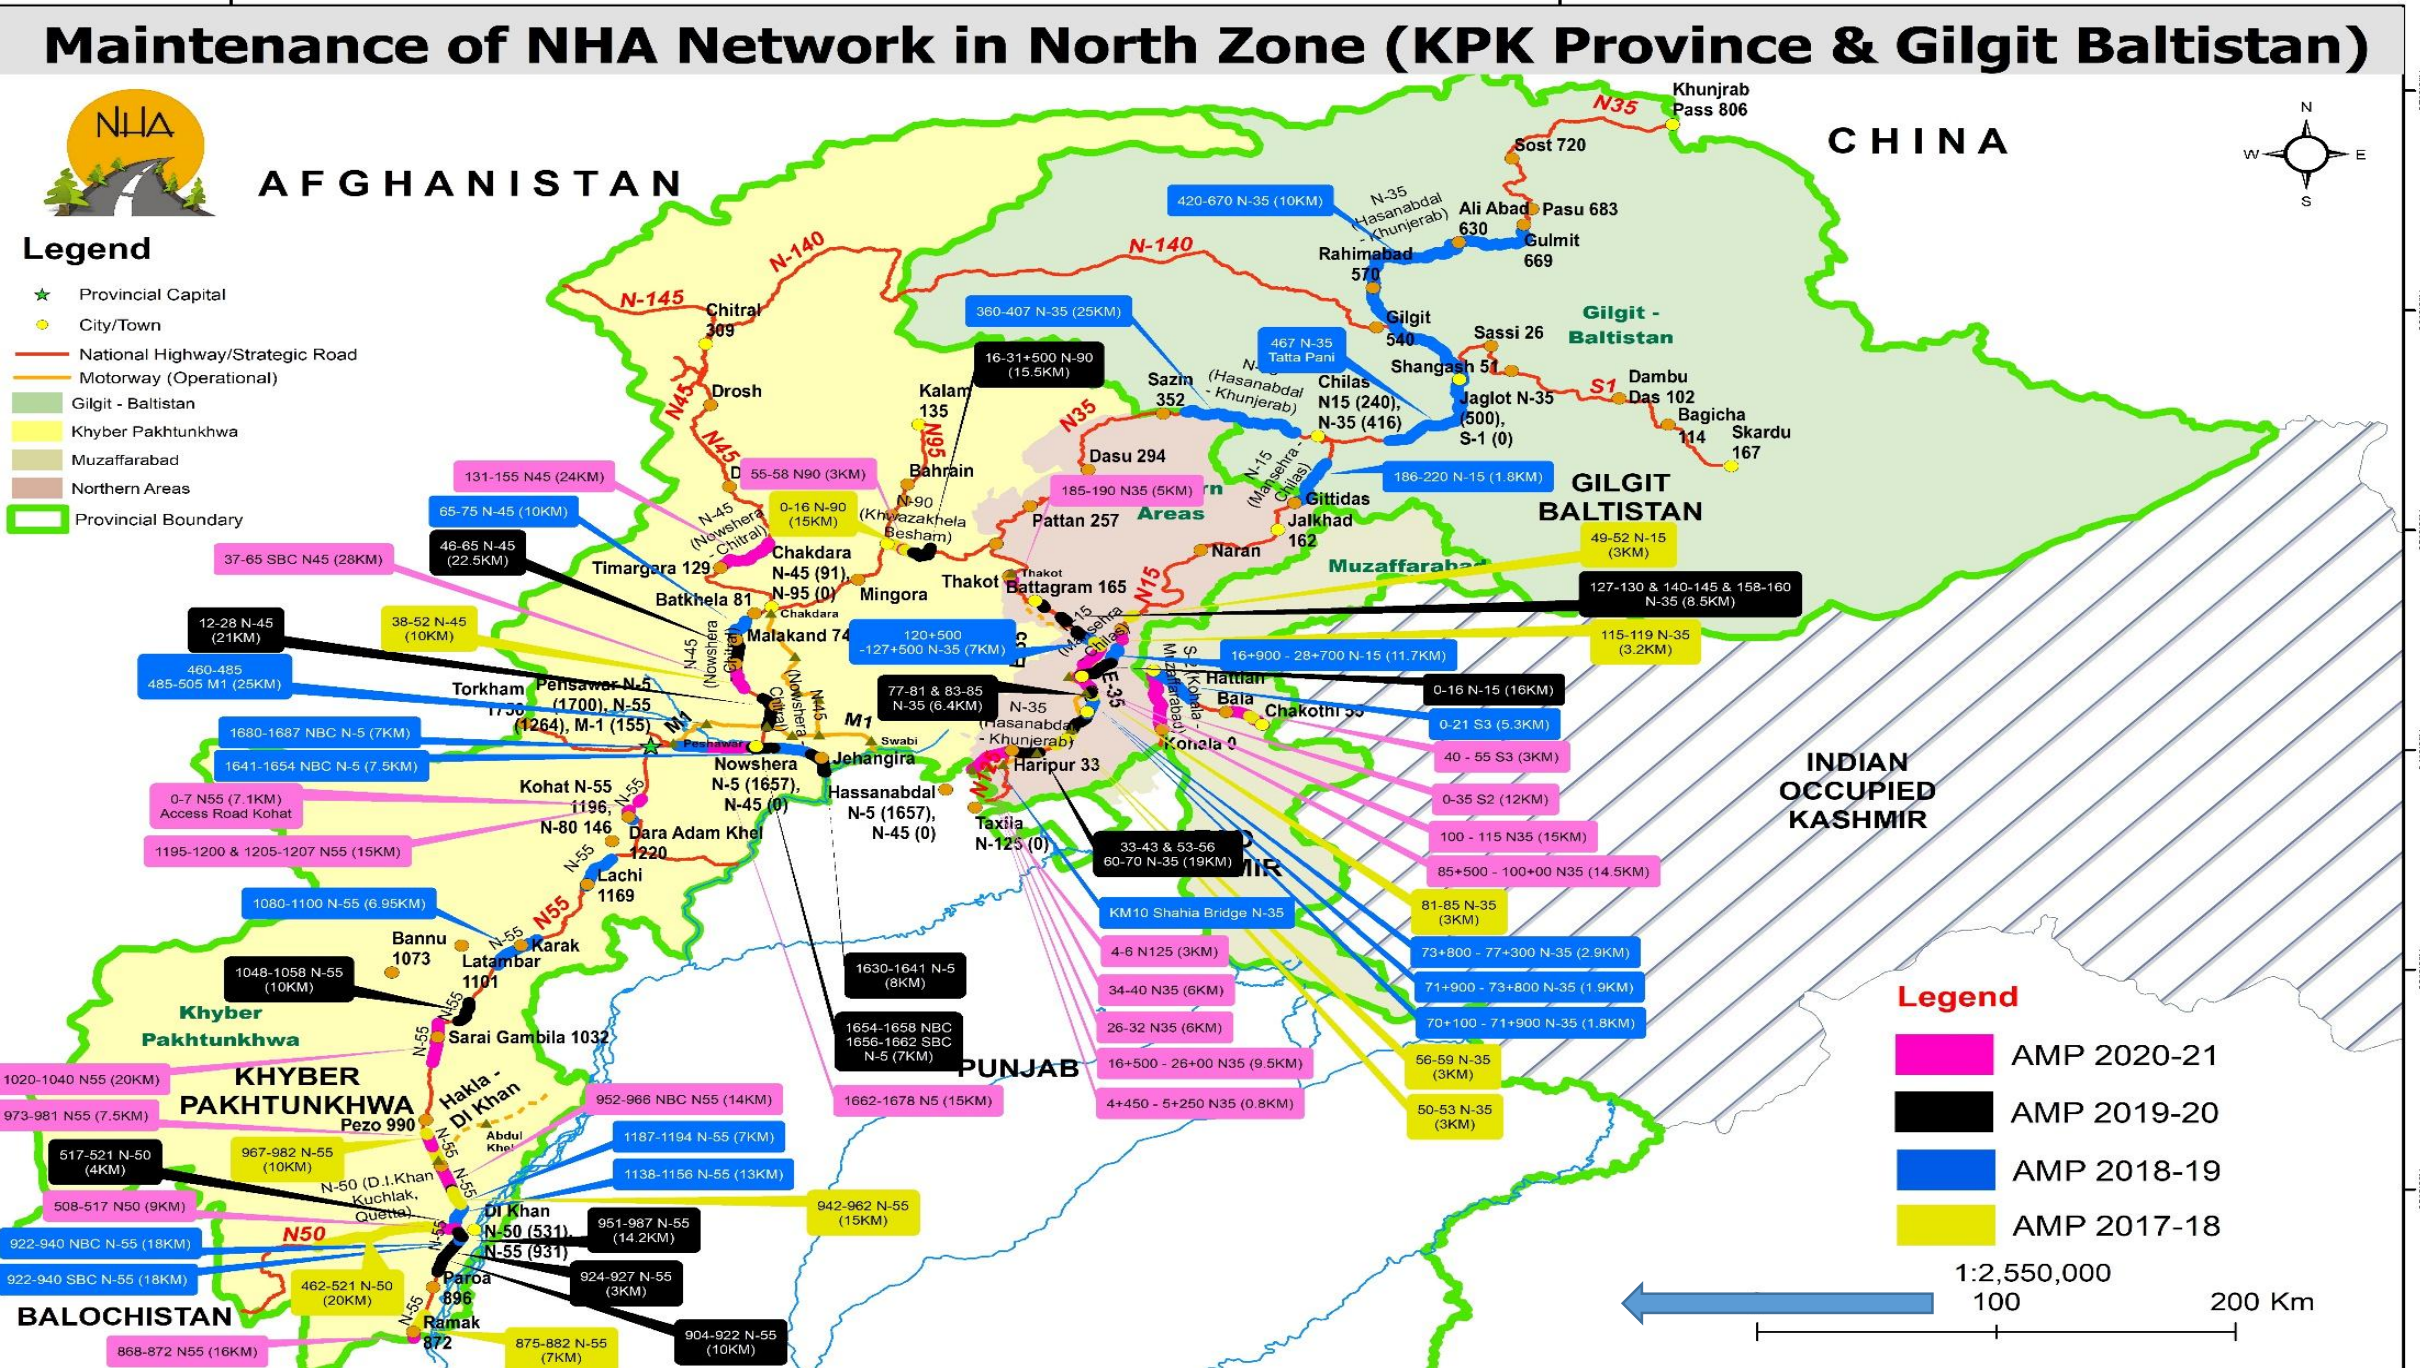


INDIAN OCCUPIED KASHMIR

Legend

- AMP 2020-21
- AMP 2019-20
- AMP 2018-19
- AMP 2017-18

1:2,550,000



Northern Areas (2017-18)

Sr No	Route	Location		Contractor	Completion Date	Cost	Progress
		From	To				
1	N-15	49.000	52.000	M/s Rustum JV DC	01.10.2019	52,239,000	Work Suspended
2	N-35	50.000	53.000	M/s Wajid Iqbal & Co	01.10.2019	45,541,000	100%
3	N-35	56.000	59.000	M/s Wajid Iqbal & Co	01.10.2019	45,541,000	100%
4	N-35	81.000	85.000	M/s Mughal Constr	01.10.2019	50,271,000	100%
5	N-35	115.000	119.000	M/s Rustum JV DC	01.10.2019	54,958,000	100%

Northern Areas (2018-19)								
Sr No	Scheme	Engr Est	Location		Contractor Name	Contract Cost	Completion Date	Progress
			From	To				
1	N-35 NBC & SBC	84.302	70+100	71+900	M/s Ugalco Construction Co.	57.721	02.05.2021	100%
2	N-35 NBC & SBC	129.116	71+900	73+800	M/s Ugalco Construction Co.	88.406	02.05.2021	95%
3	N-35 NBC & SBC	140.242	73+800	77+300	M/s Ugalco Construction Co.	96.024	02.05.2021	90%
4	N-35	207.161	120+500	127+500	M/s Ugalco Construction Co.	141.843	16.08.2021	25%
5	N-15 - Km. 16+900 - 28+700	262.944	16+900	28+700	M/s Mohammad Construction Co.	179.364	18.07.2021	42%
6	N35 Shahia Bridge	160	10+00			178 Days		

Northern Areas (2019-20)

Sr No	Scheme	Engineer's Estimate	T.S Date	Procurement Status		Award Date (Expected)	Completion Time	Completion Date (Expected)
				TBER Status	PBER Status			
1	N-35 Km 33+500 - 43+000, KM 53+00 - 56+00 & KM 60+00 - 70+300	486.706	3/12/2020	Approved	Under Process	Aug-21	178 Days	Feb-2022
2	N-35 - Km. 77+300 - 81+000 & 83+300 - 85+000	161.06	3/12/2020	Approved	Under Process	Aug-21	178 Days	Feb-2022
3	N-35 - Km. 127+500 - 130, 140+00 - 145+00 & 158+800 - 160+200	232.42	3/12/2020	Approved	Under Process	Aug-21	178 Days	Feb-2022
4	N-15 - Km. 000 - 16+900	324.186	3/12/2020	Approved	Under Process	Aug-21	178 Days	Feb-2022

Northern Areas (2020-21)


Sr No	Scheme	Eng Est (Million)	T.S Date (Expected)	Procurement Status	Award Date (Expected)	Completion Time	Completion Date (Expected)
1	KM 185+000-190+000 on N-35	84.302	20/5/2021	To be Procured	20/10/2021	178 Days	30/6/2022
2	KM 4+450-5-250 on N-35	18.359	20/5/2021	To be Procured	20/10/2021	178 Days	30/6/2022
3	KM 16+500-26+000 on N-35	395.077	20/5/2021	To be Procured	20/10/2021	178 Days	30/6/2022
4	KM 26+000-32+000 on N-35	343.14	20/5/2021	To be Procured	20/10/2021	178 Days	30/6/2022
5	KM 85+500-100+000 on N-35	372.252	20/5/2021	To be Procured	20/10/2021	178 Days	30/6/2022
6	KM 100+000-115+000 on N-35	347.907	20/5/2021	To be Procured	20/10/2021	178 Days	30/6/2022
7	KM 34+000-40+000 on N-15	311.474	20/5/2021	To be Procured	20/10/2021	178 Days	30/6/2022
8	KM 4+000-6+000 on N-125	152.76	20/5/2021	To be Procured	20/10/2021	178 Days	30/6/2022

Maintenance of NHA Network in North Zone (KPK Province & Gilgit Baltistan)




AFGHANISTAN

CHINA



Legend

- ★ Provincial Capital
- City/Town
- National Highway/Strategic Road
- Motorway (Operational)
- Gilgit - Baltistan
- Khyber Pakhtunkhwa
- Muzaffarabad
- Northern Areas
- Provincial Boundary

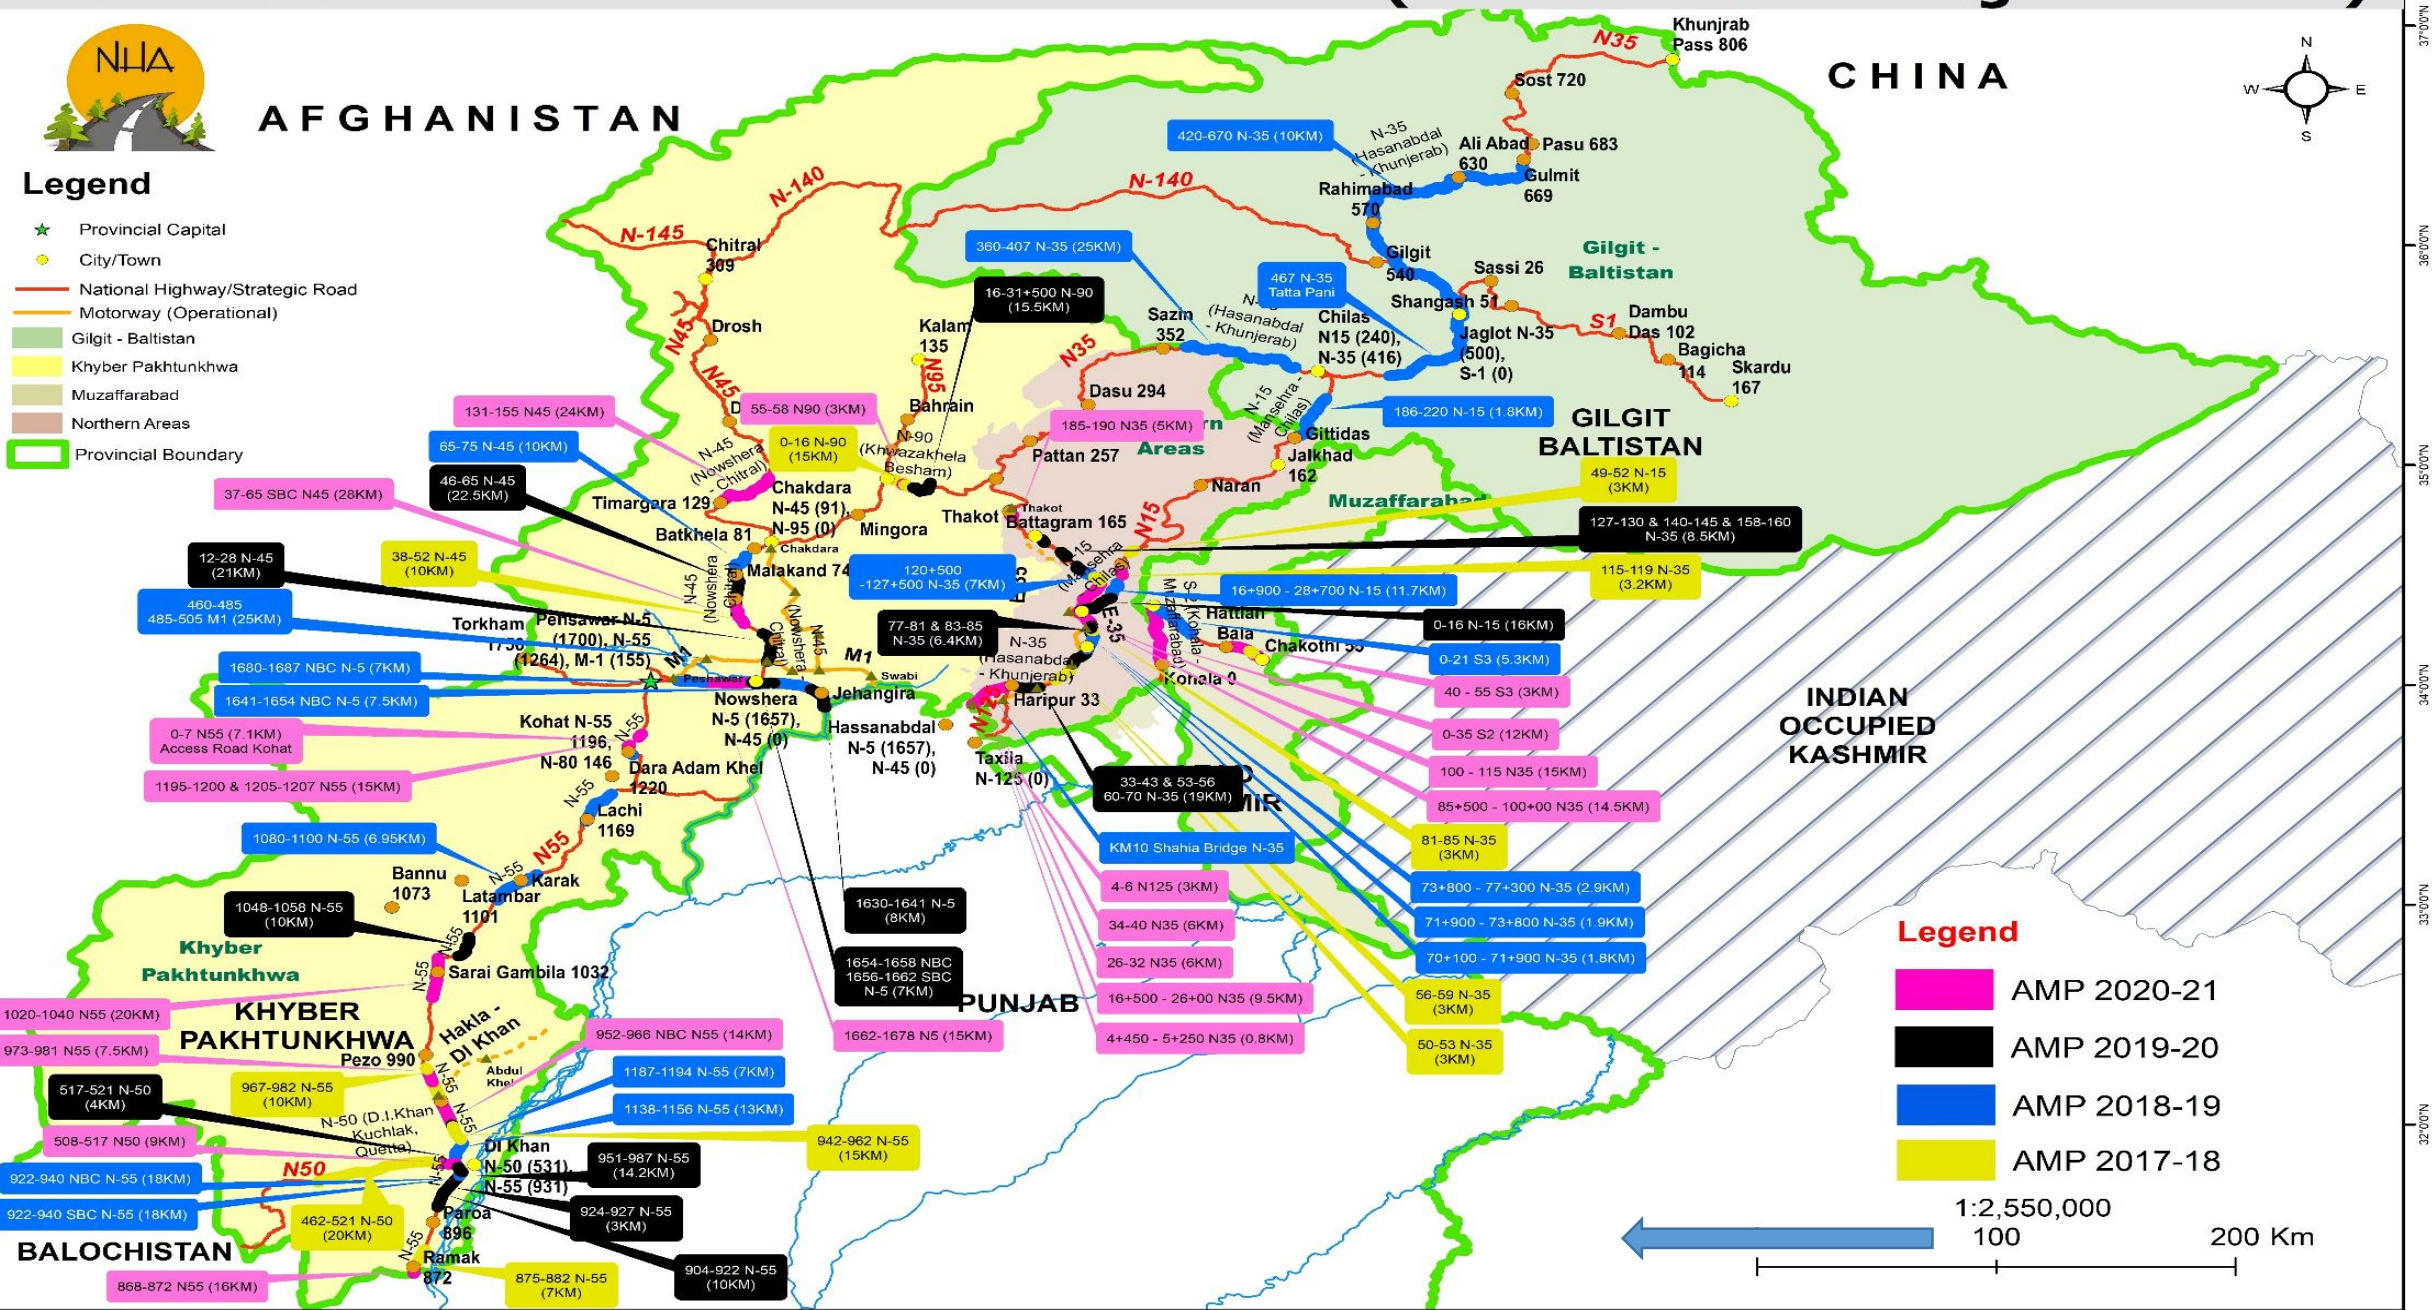

INDIAN OCCUPIED KASHMIR

Legend

- AMP 2020-21
- AMP 2019-20
- AMP 2018-19
- AMP 2017-18

1:2,550,000



Gilgit-Baltistan (2017-18)

Sr No	Route	Location		Contractor	Completion Date	Cost	Progress
		From	To				
1	N-15	216.000	240.000	M/s RADC	19.01.2020	120,953,547	90%
2	N-35	417.000	444.000	M/s RADC	31.05.2021	184,406,032	76%

Gilgit-Baltistan (2018-19)								
Sr No	Scheme	Engr Est	Location		Contractor Name	Contract Cost	Completion Date	Progress
			From	To				
1	N-35 (Deposit Works)	513.920	300+00	315+00	M/s Rustam Associates JV M/s Dynamic Construction	400.343	08-08-2021	20%
2	N-35 (Deposit Works)	448.014	315+00	330+00	M/s Rustam Associates JV M/s Dynamic Construction	362..443	08.08.2021	25%
3	N-35 (Deposit Works)	434.566	333+00	350+00	M/s Hilton Const JV M/s HRK & Co	322.505	07.06.2021	25%
4	N-35 (Deposit Works)	657.585	360+00 372+00	367+500 387+500	M/s Hilton Const JV M/s HRK & Co	488.020	07.06.2021	15%
5	N-35 (Deposit Works)	306.310	387+500	397+500	M/s Hilton Const JV M/s HRK & Co	214.723	07.06.2021	18%
6	N-35 (Deposit Works)	250.002	397+500	406+500	M/s Rustam Associates JV M/s Dynamic Construction	175.2518	08.08.2021	25%

Gilgit Baltistan (2019-20)

Sr No	Scheme	Eng Est (Million)	T.S Date (Expected)	Procurement Status	Award Date (Expected)	Completion Time	Completion Date (Expected)	
Total	Nil	-	-	-	-	-	-	

Gilgit Baltistan (2020-21)


Sr No	Scheme	Eng Est (Million)	T.S Date (Expected)	Procurement Status	Award Date (Expected)	Completion Time	Completion Date (Expected)
1	Nil	-	-	-	-	-	-

Maintenance of NHA Network in North Zone (KPK Province & Gilgit Baltistan)




AFGHANISTAN

CHINA



Legend

- ★ Provincial Capital
- City/Town
- National Highway/Strategic Road
- Motorway (Operational)
- Gilgit - Baltistan
- Khyber Pakhtunkhwa
- Muzaffarabad
- Northern Areas
- Provincial Boundary

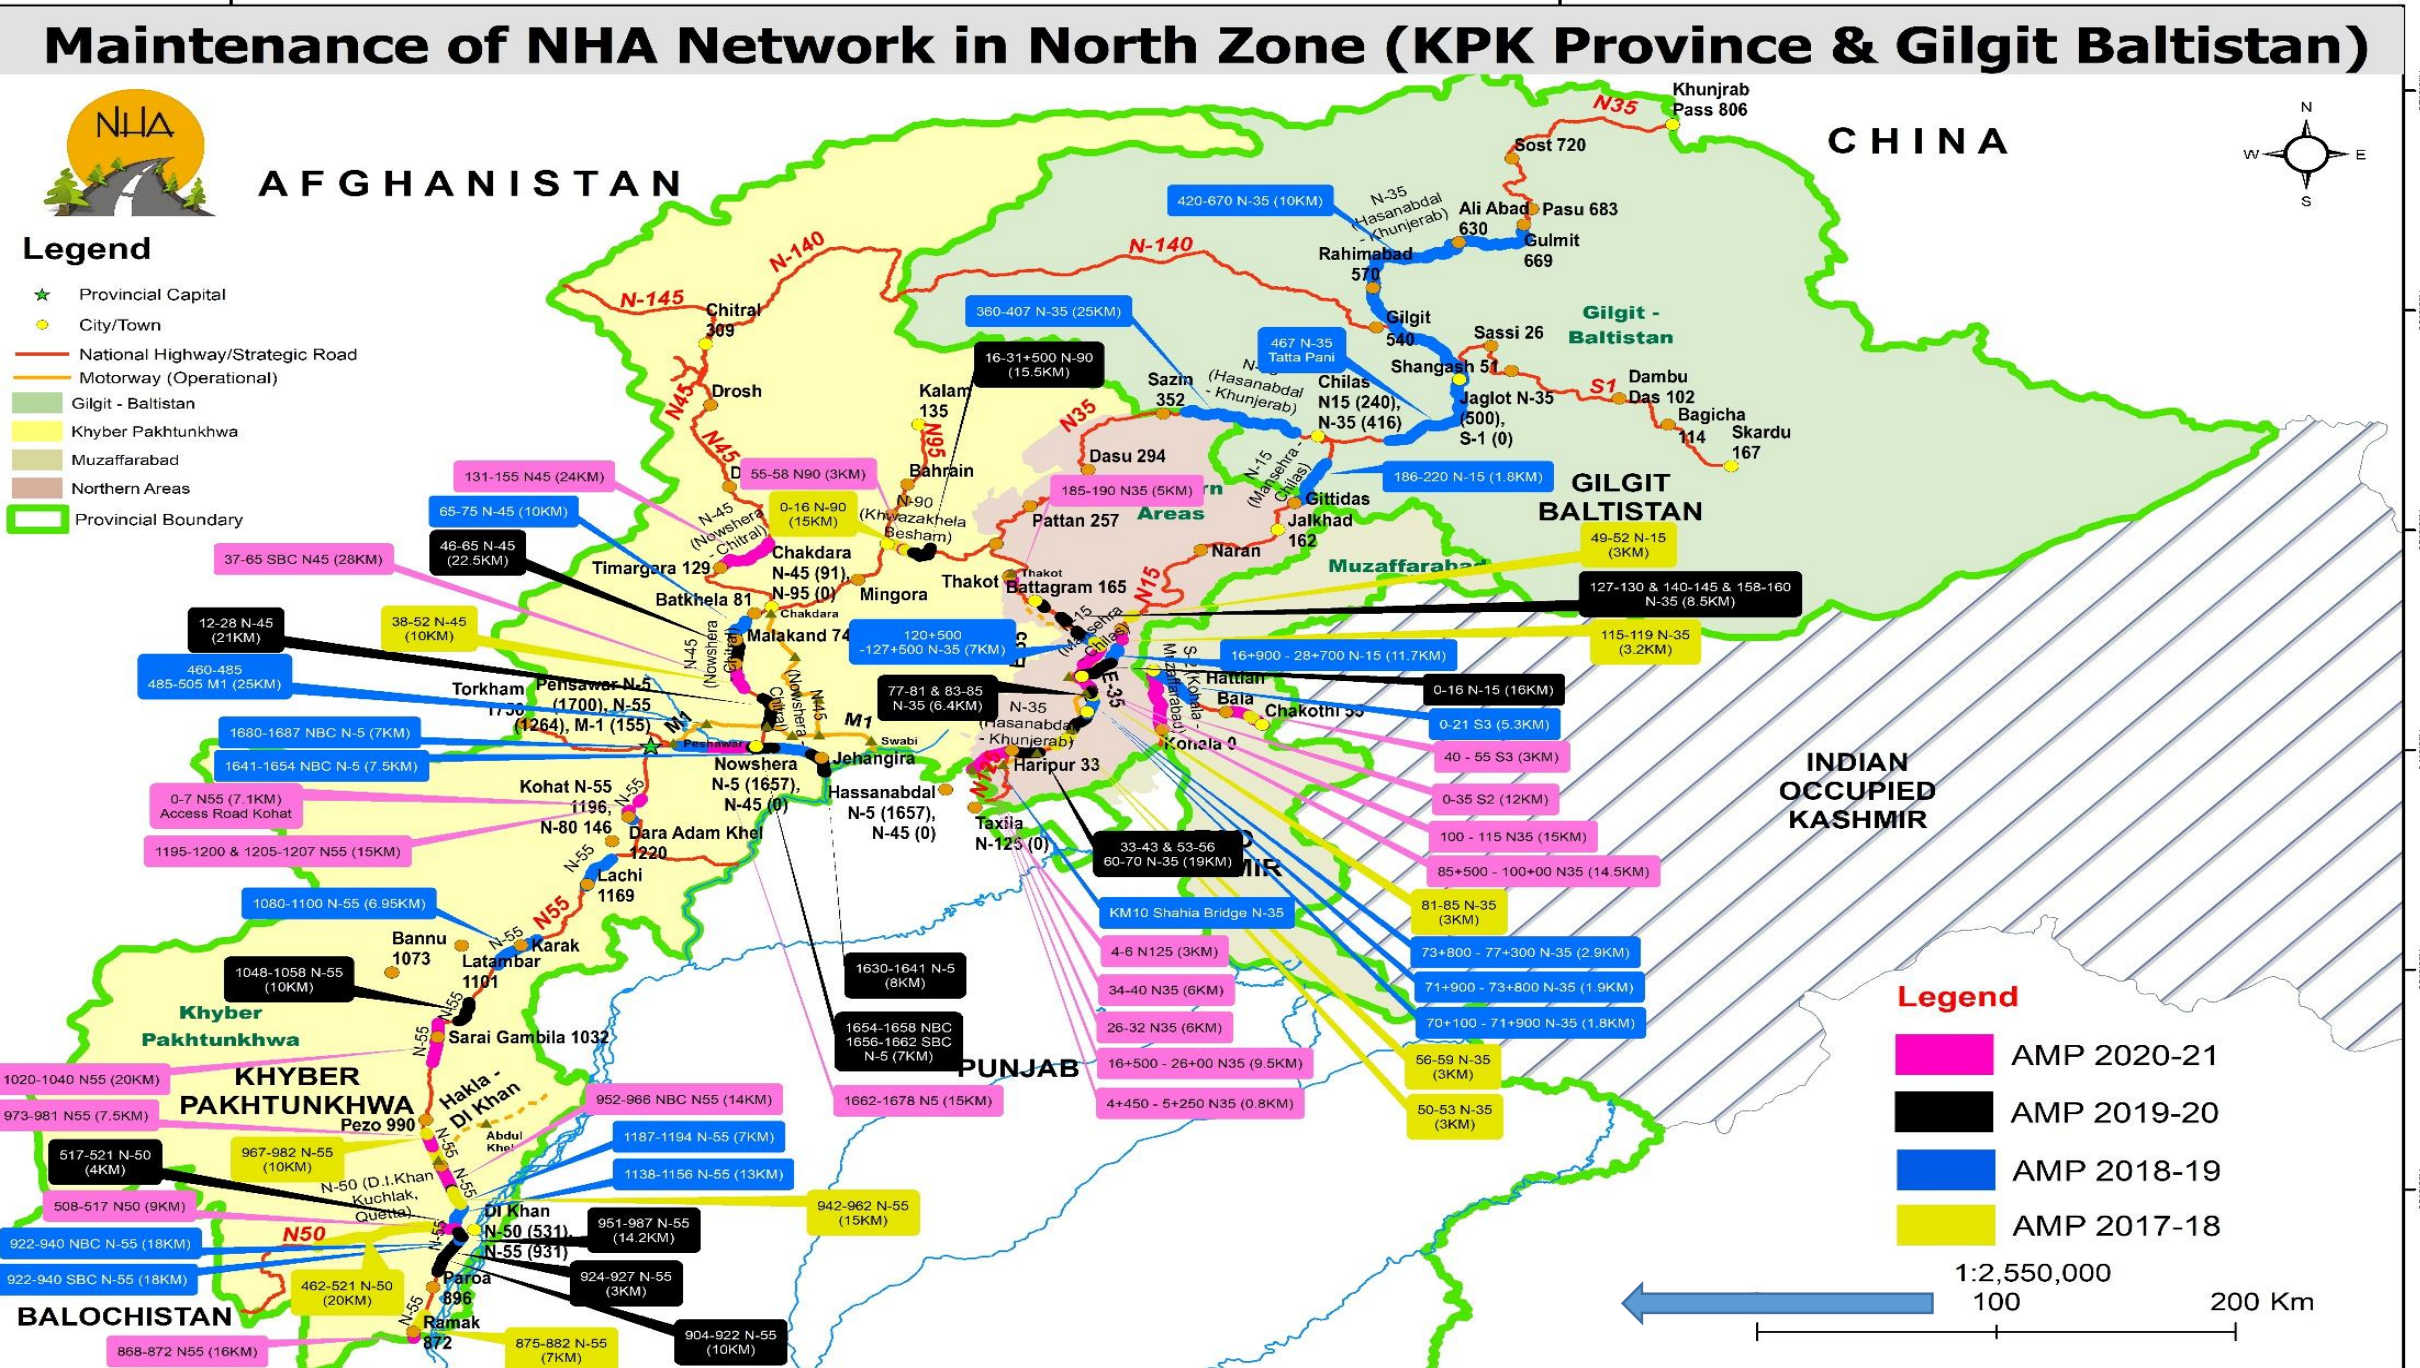

INDIAN OCCUPIED KASHMIR

Legend

- AMP 2020-21
- AMP 2019-20
- AMP 2018-19
- AMP 2017-18

1:2,550,000

